

TIME SQUARE 10 SHV REPORT

09 September 2026

TIME SQUARE 10 SHV LOCATION



TIME SQUARE 10 SHV LOCATION



TIME SQUARE 10 SHV ANOTHER POINT OF VIEW



TIME SQUARE 10 SHV FLOOR PLAN



TOOL BOX MEETING






MEETING WITH CONCRETE TEAM







BREAKING PILE-HEAD PROGESS UP TO 09 SEPTEMBER 2026
126/197pcs

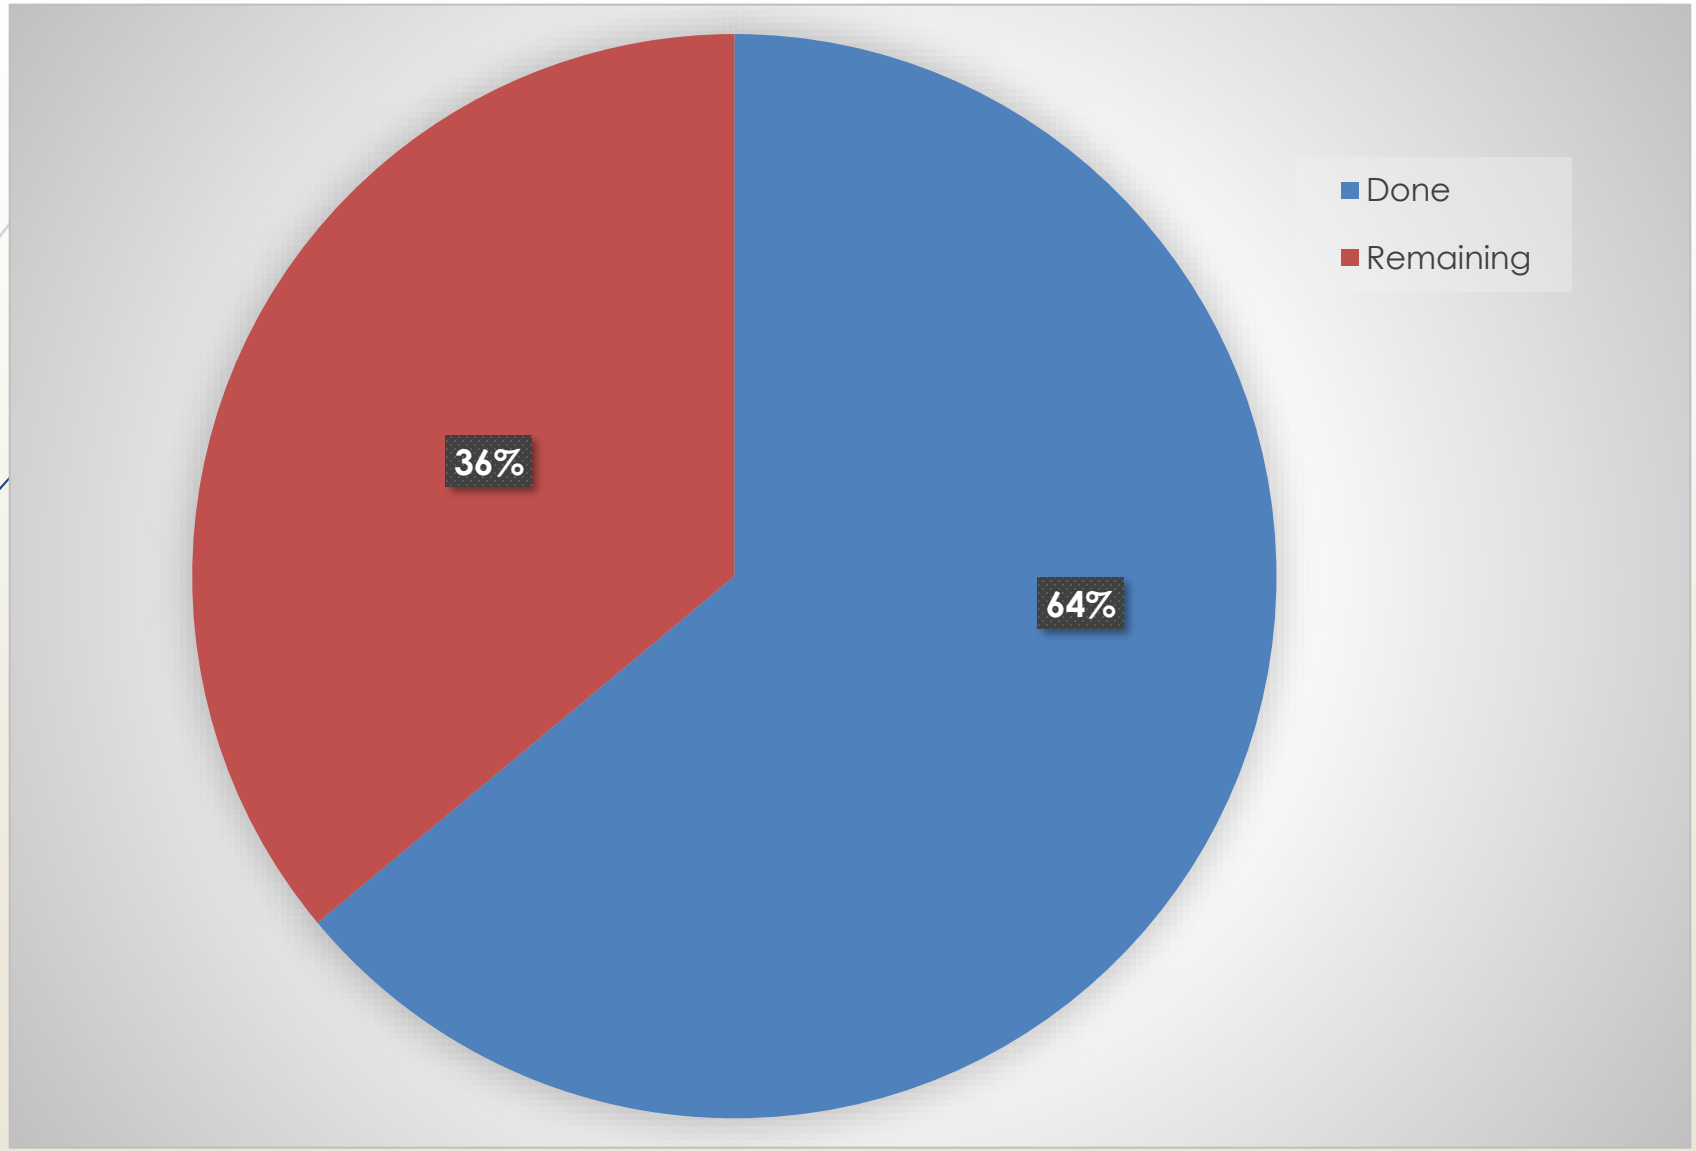

PILECAP FINISHED PROGESS UP TO 09 SEPTEMBER 2026
17/28pc

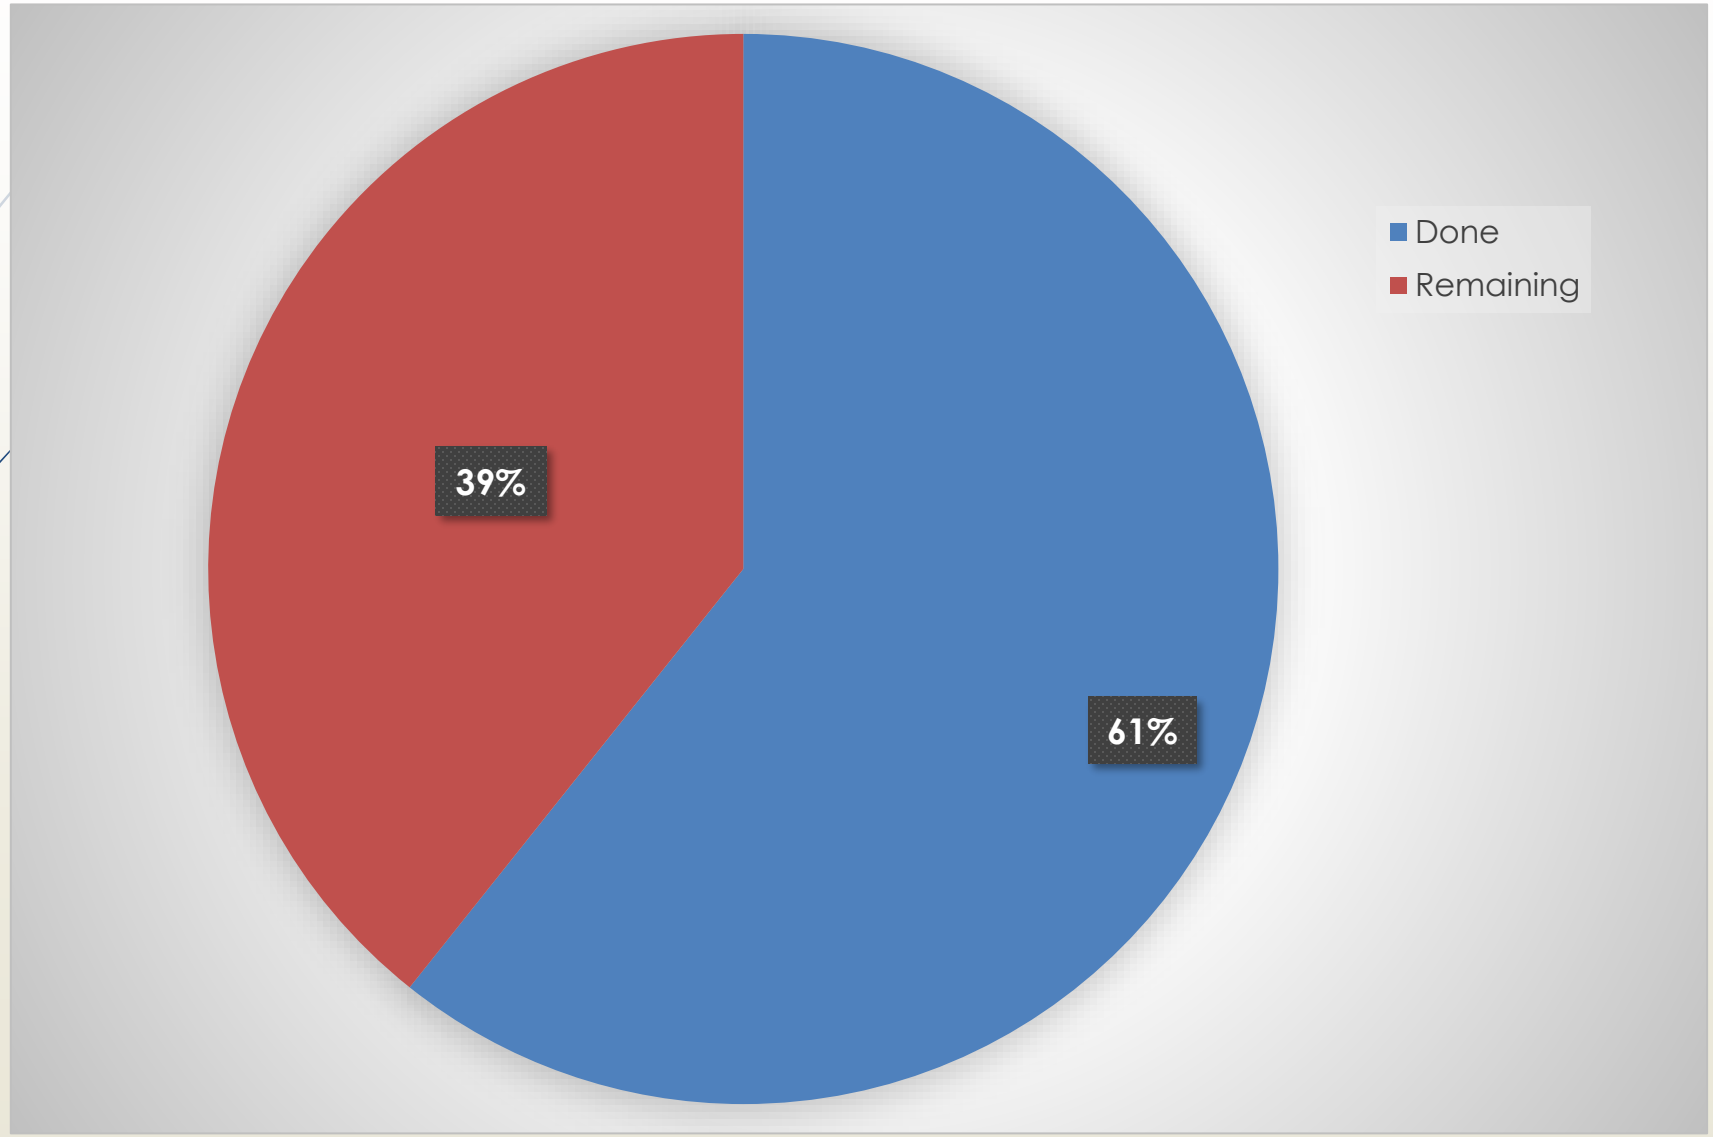


BREAKING PILE-HEAD AND COMPLETED PILECAP PROGESS UP TO 09 SEPTEMBER 2026

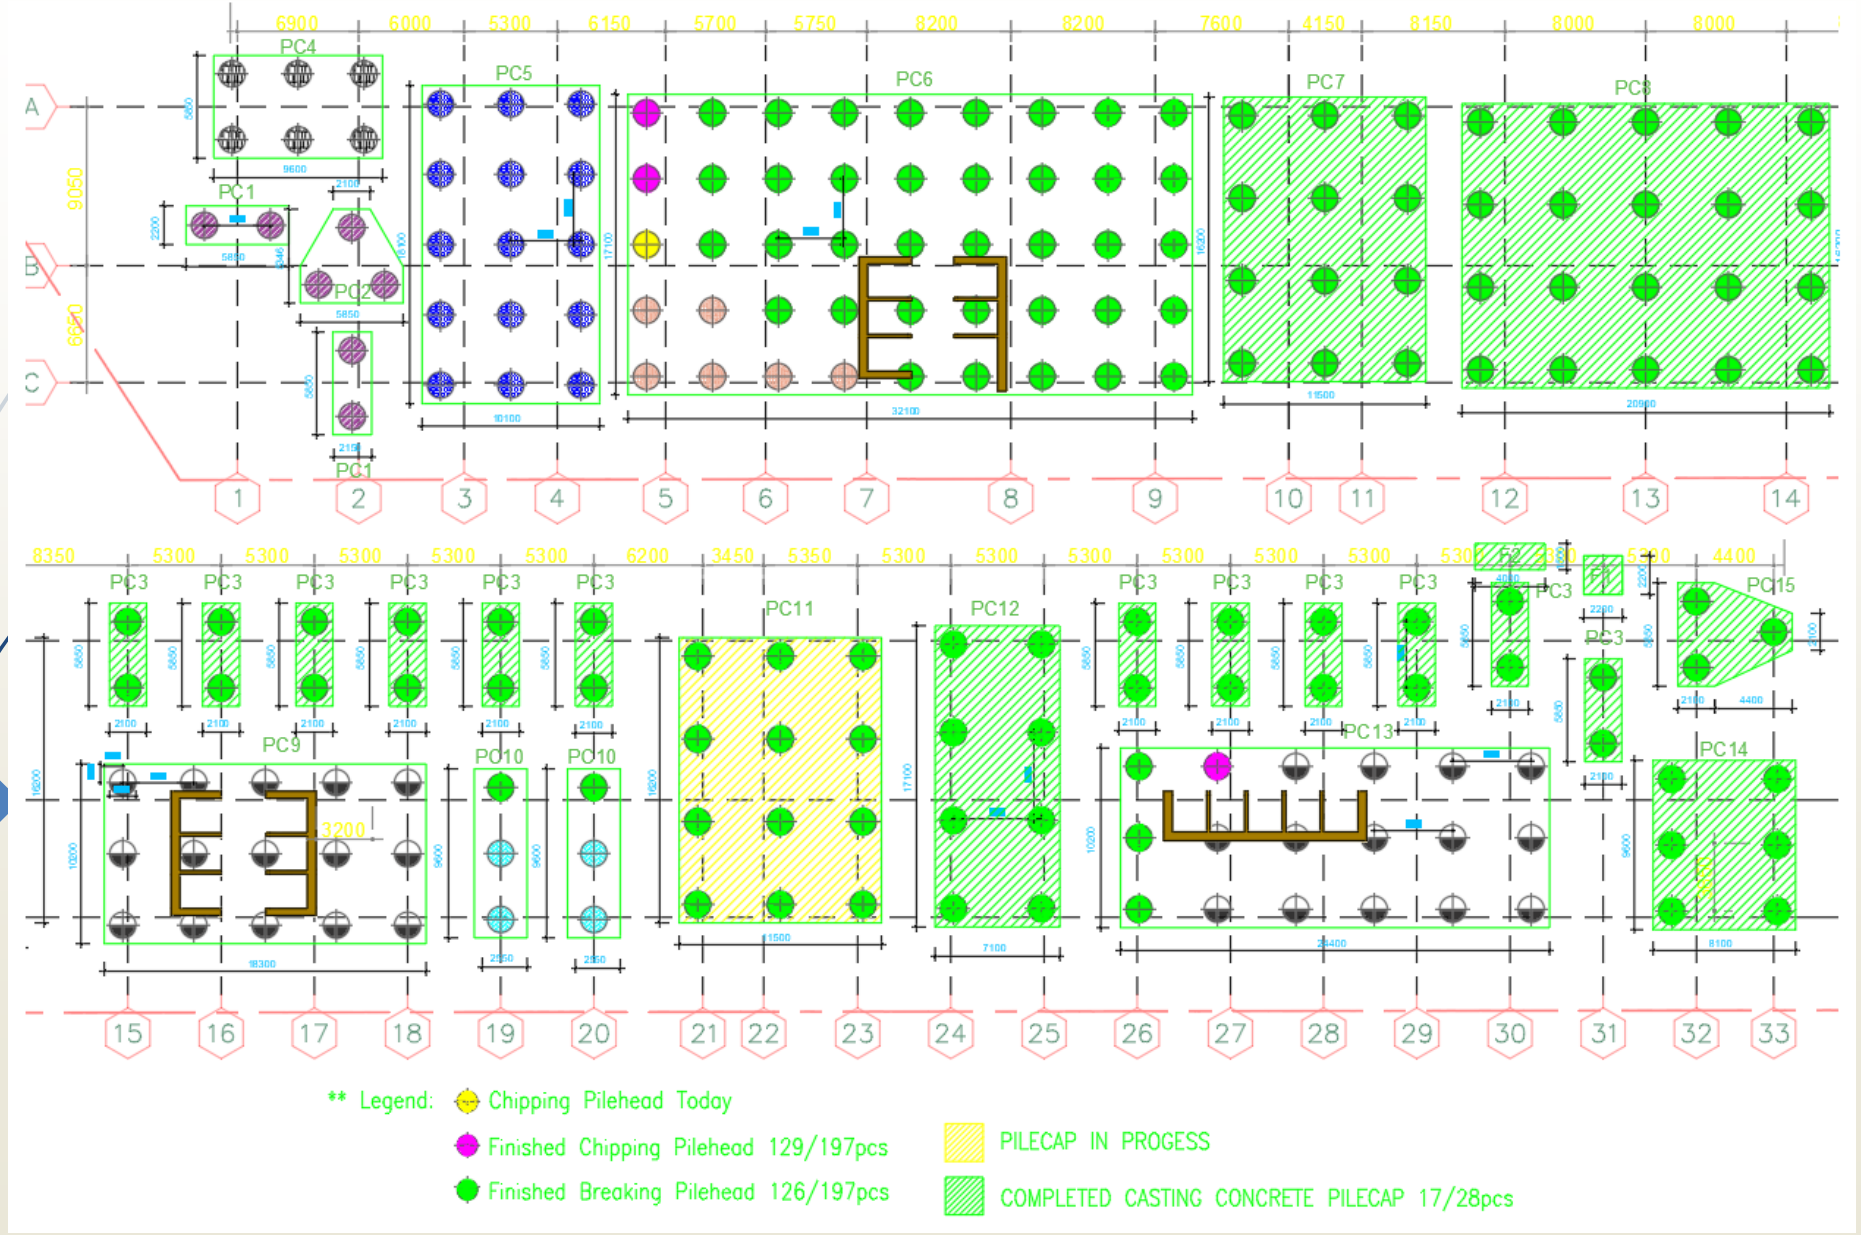

BREAKING UNDERGROUND STONE EXCAVATE FOR PC6, PC11, PC12 & PC13



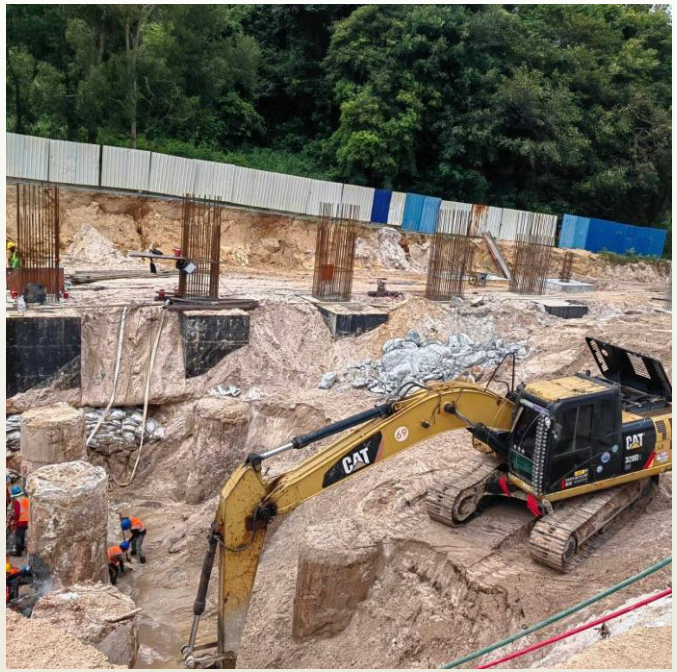



CHIPPING PILE-HEAD PC6, PC10 & PC13








INSPECTION REBAR PC14









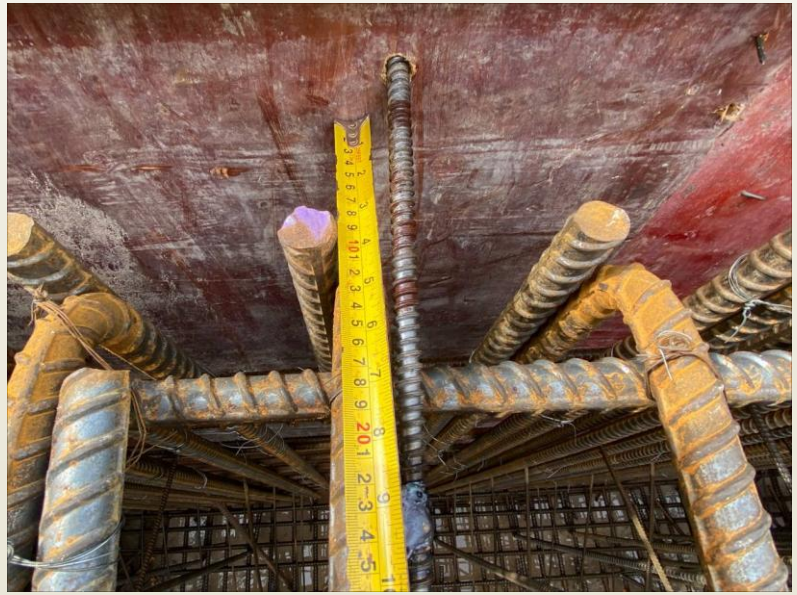

CONCRETE INSPECTION FOR PC14











CASTING CONCRETE PC14

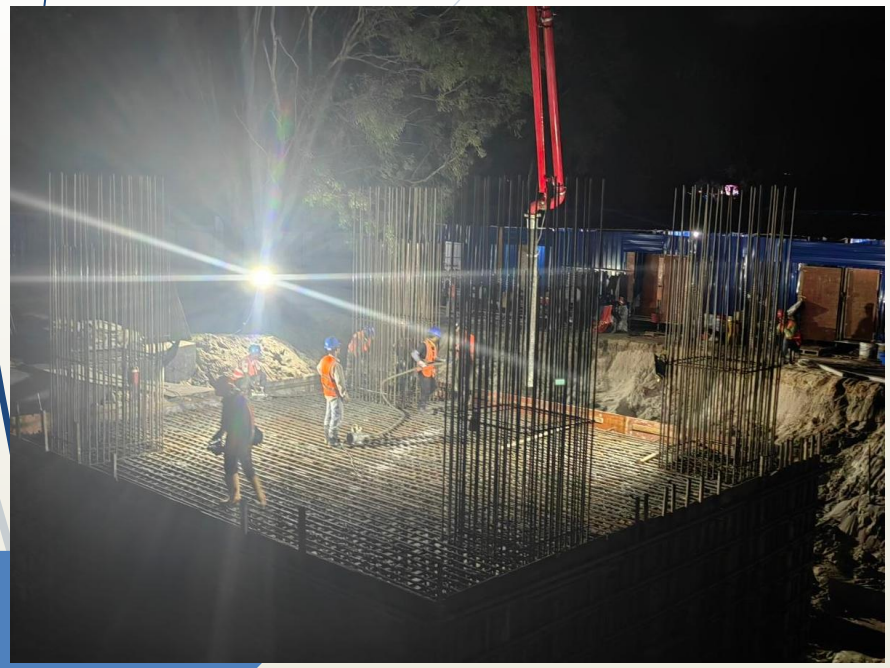

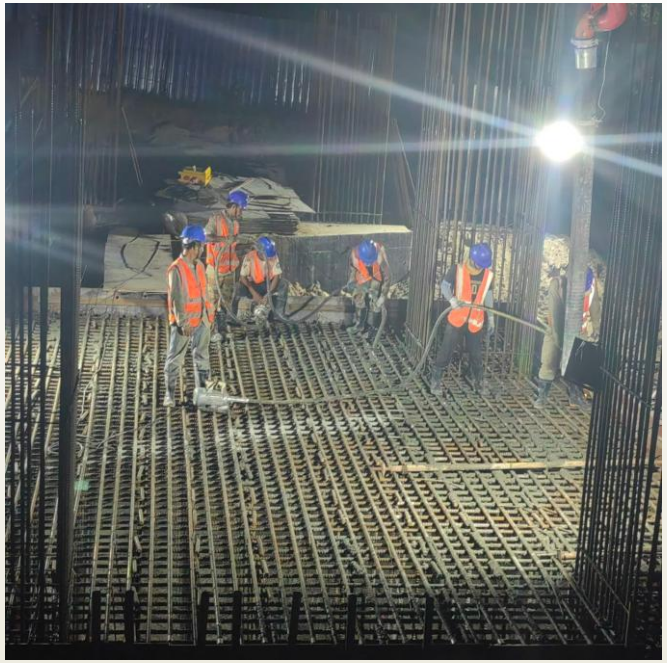



REMOVING FORMWORK AND SOIL BACKFILL PC14








INSPECTION REBAR F1 & F2




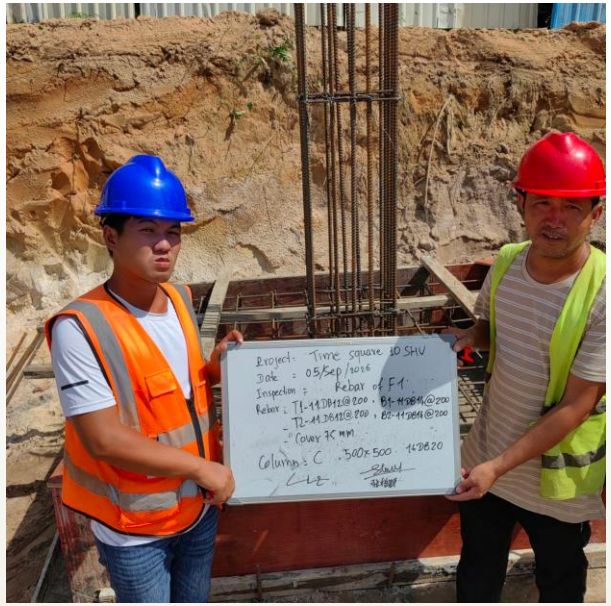







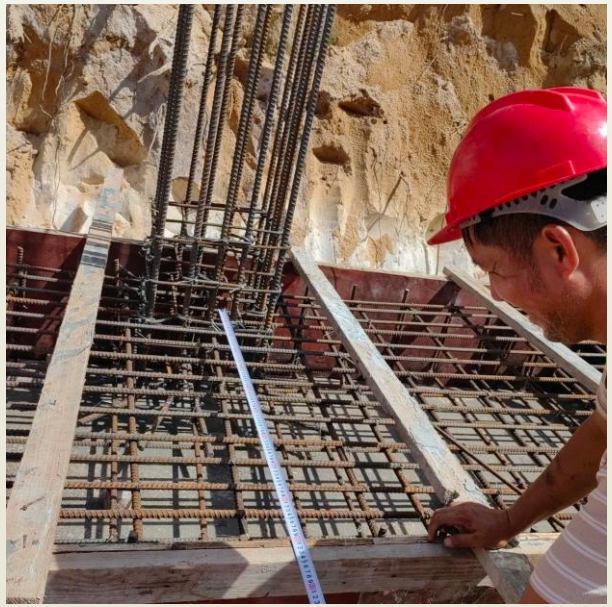

CONCRETE INSPECTION FOR F1 & F2











INSPECTION REBAR PC12





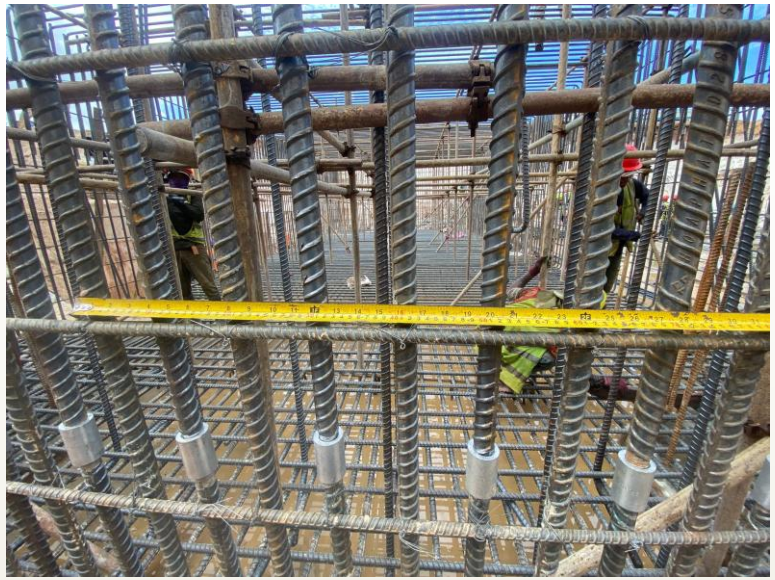

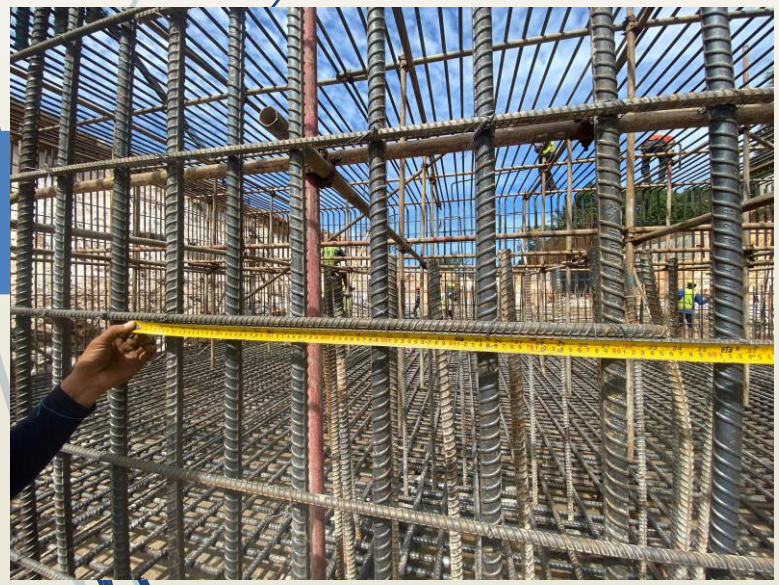





CONCRETE INSPECTION FOR PC12













SOIL DEPOSAL





MATERIAL ARRIVED ON SITE









SITE ENVIRONMENT







PASSION FOR PROGRESS!

TIME SQUARE 10

OCEAN VIEW

THE BEST DAY IN OTRES BEACH

THANK YOU!
