


# TIME SQUARE 10 SHV REPORT

19 September 2026

# TIME SQUARE 10 SHV LOCATION



# TIME SQUARE 10 SHV LOCATION



# TIME SQUARE 10 SHV ANOTHER POINT OF VIEW



# TIME SQUARE 10 SHV FLOOR PLAN



# TOOL BOX MEETING






# MEETING WITH CONCRETE TEAM







# BREAKING PILE-HEAD PROGESS UP TO 19 SEPTEMBER 2026
# 151/197pcs

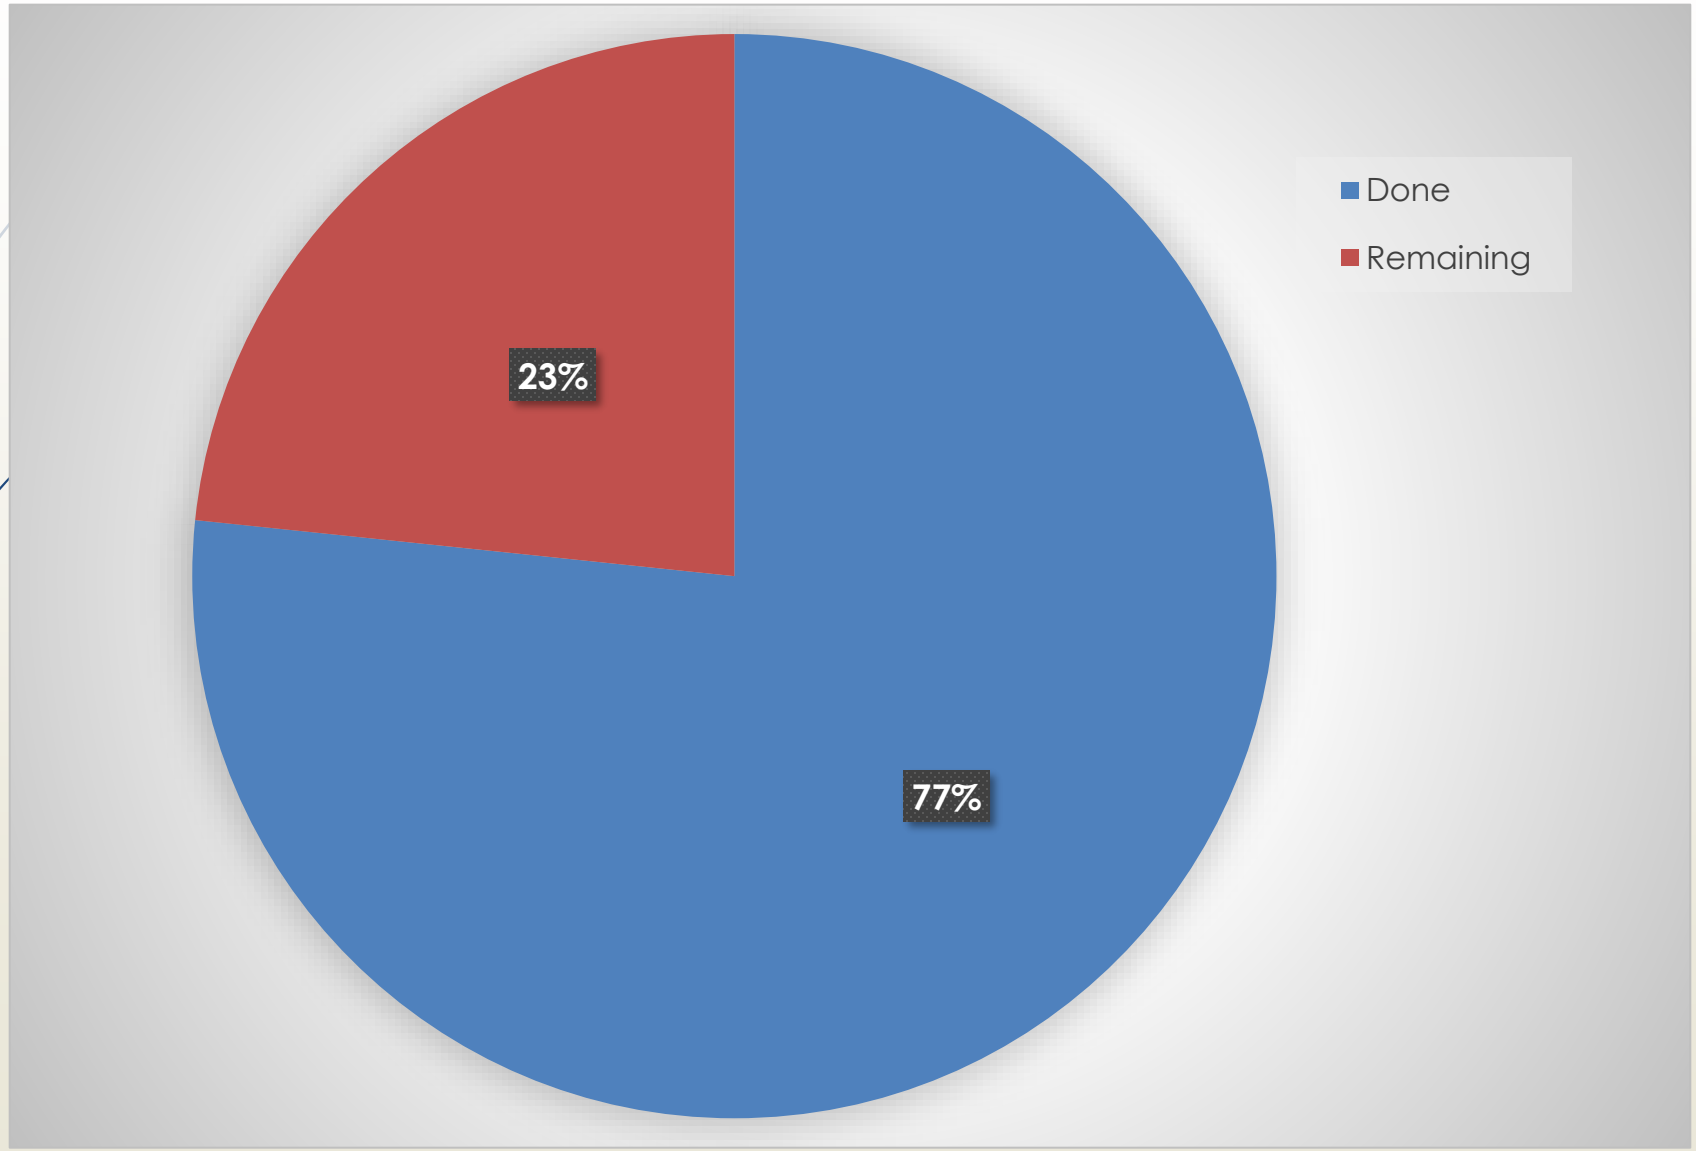

# PILECAP FINISHED PROGESS UP TO 19 SEPTEMBER 2026
# 20/28pc

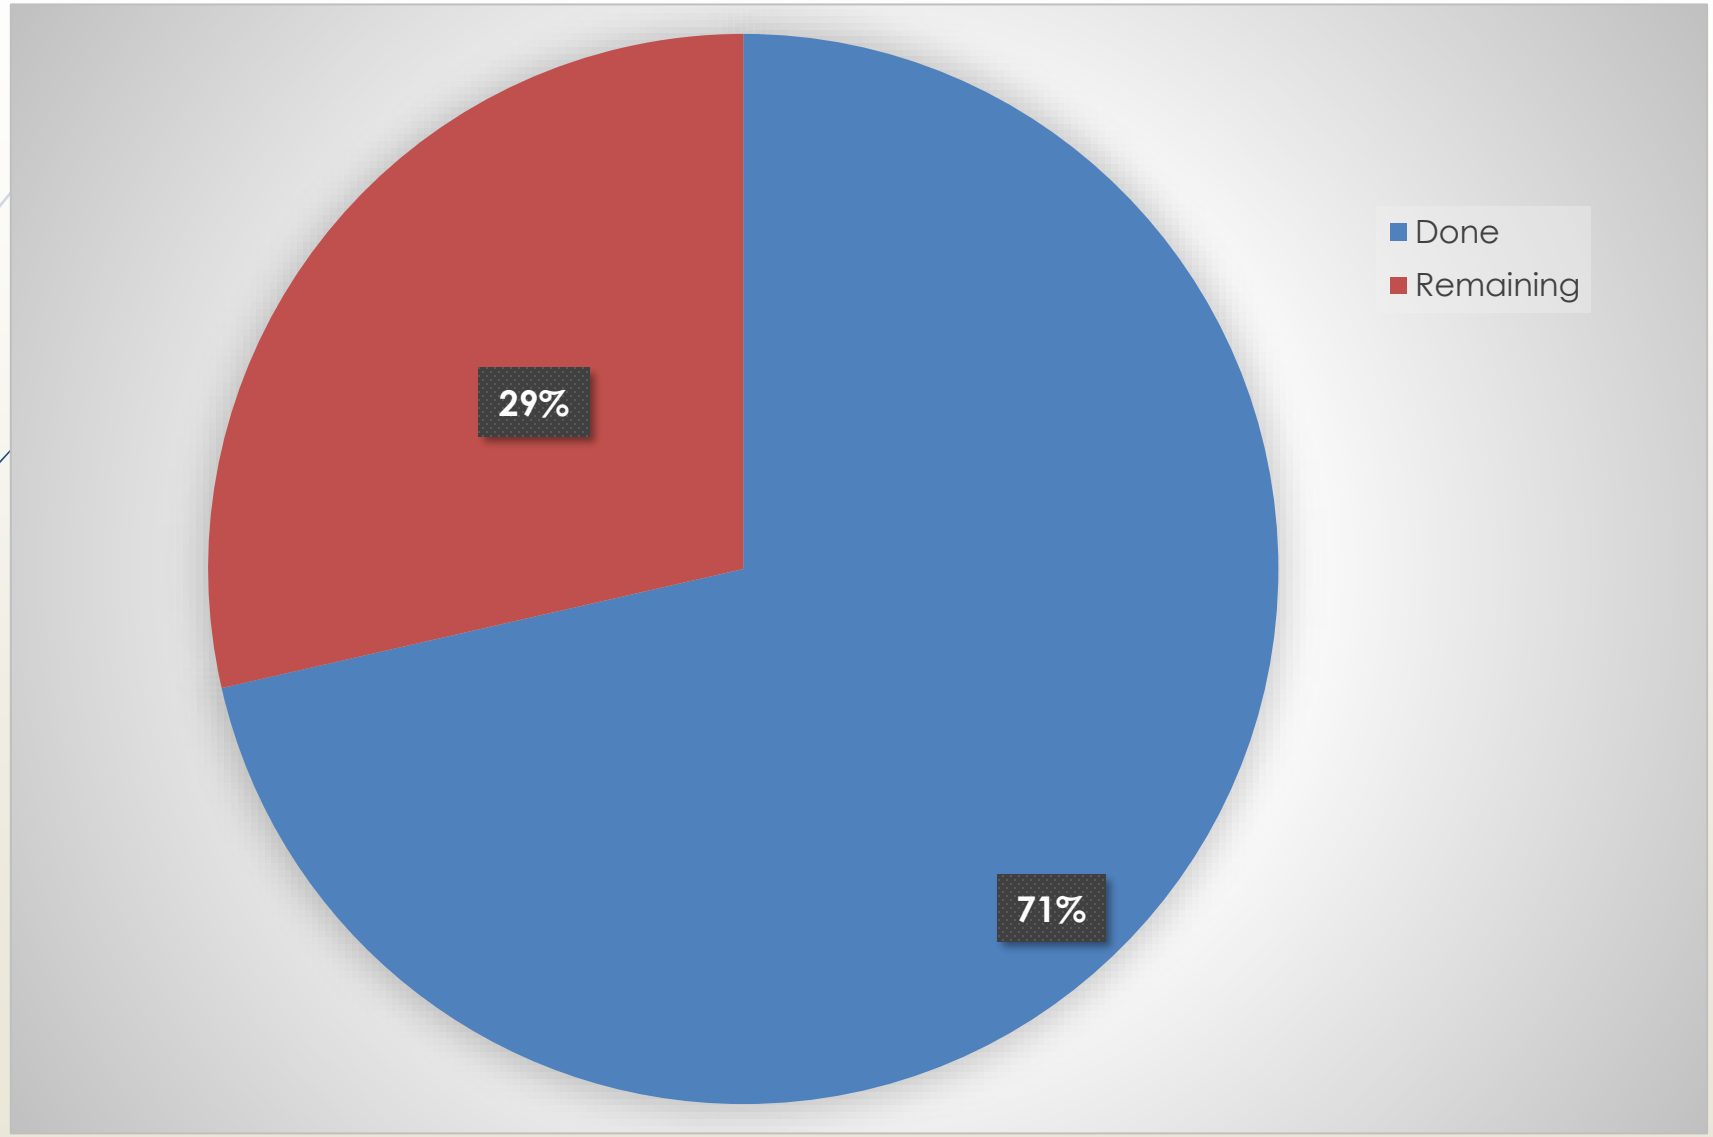

# BREAKING PILE-HEAD AND COMPLETED PILECAP PROGESS UP TO 19 SEPTEMBER 2026

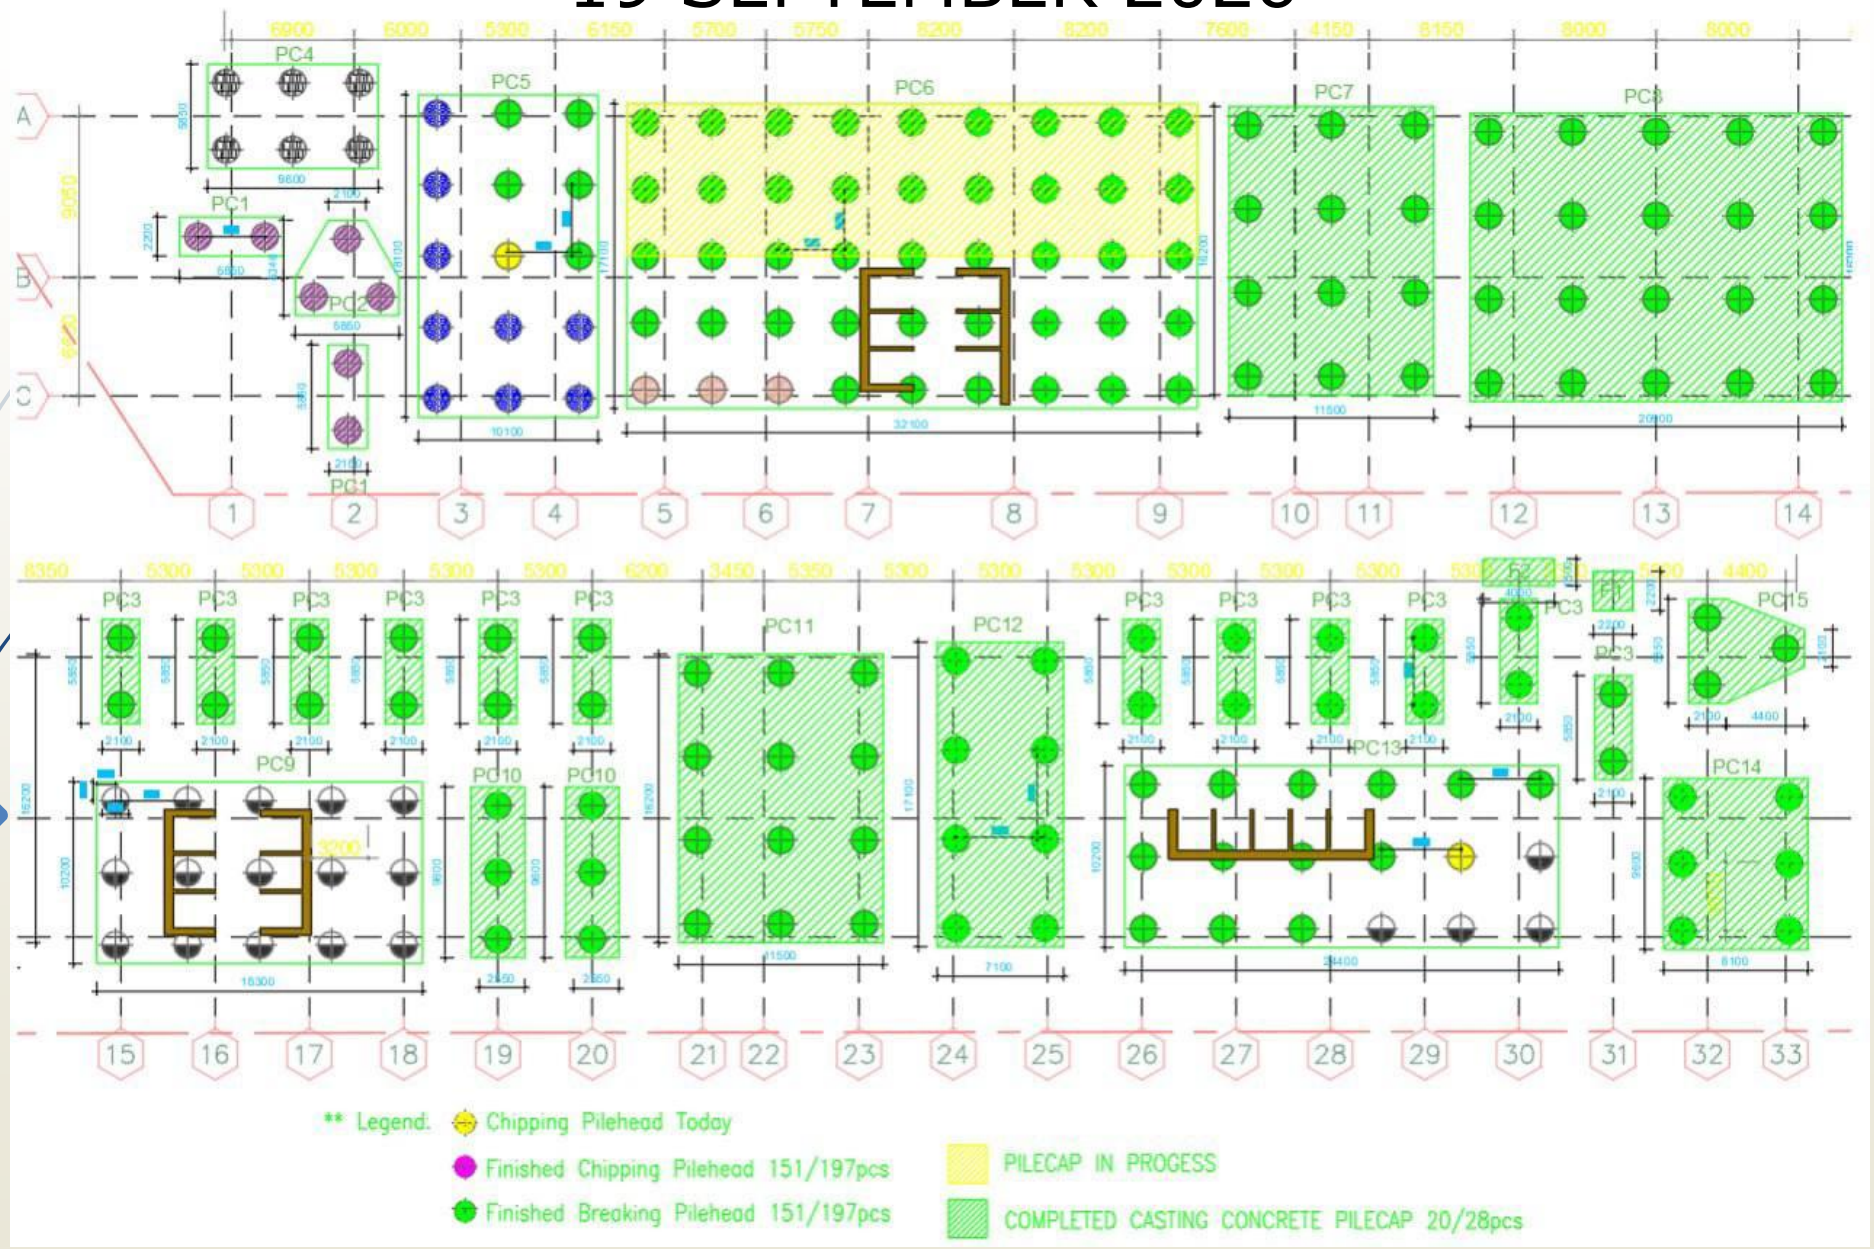

# BREAKING UNDERGROUND STONE EXCAVATE FOR PC5, PC6 & PC13










# CHIPPING PILE-HEAD PC5, PC6 & PC13

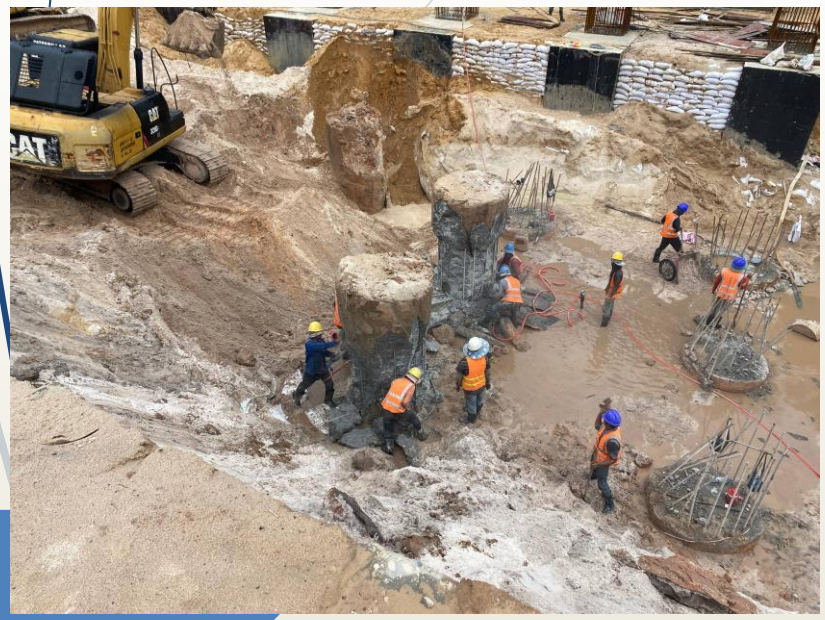






# INSTALLING GROUNDING SYSTERM





# INSPECTION REBAR PC11



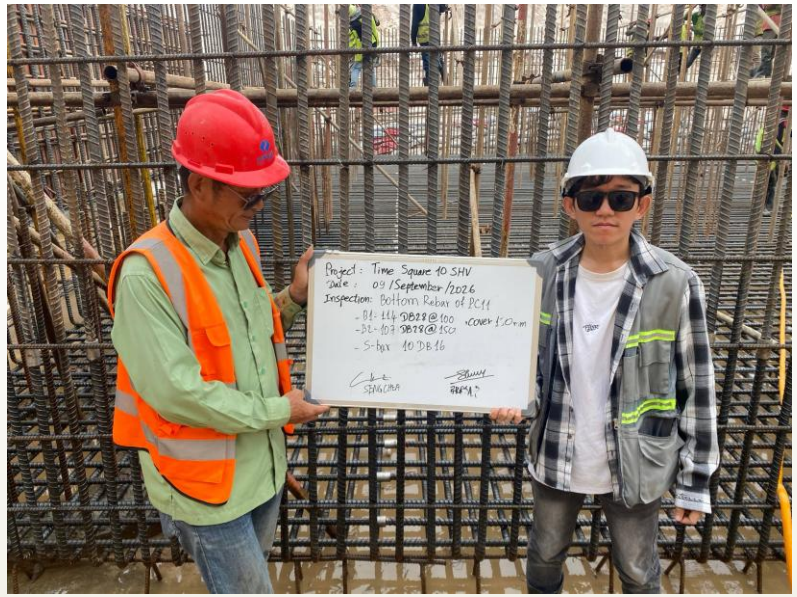








# CASTING CONCRETE PC11














# INSPECTION REBAR PC10 x2PC











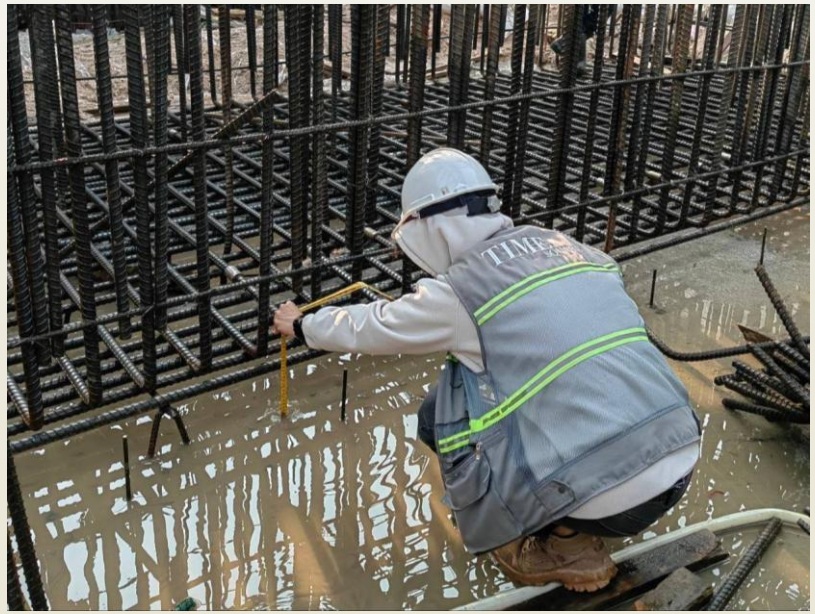


# CONCRETE INSPECTION PC10 x2PC



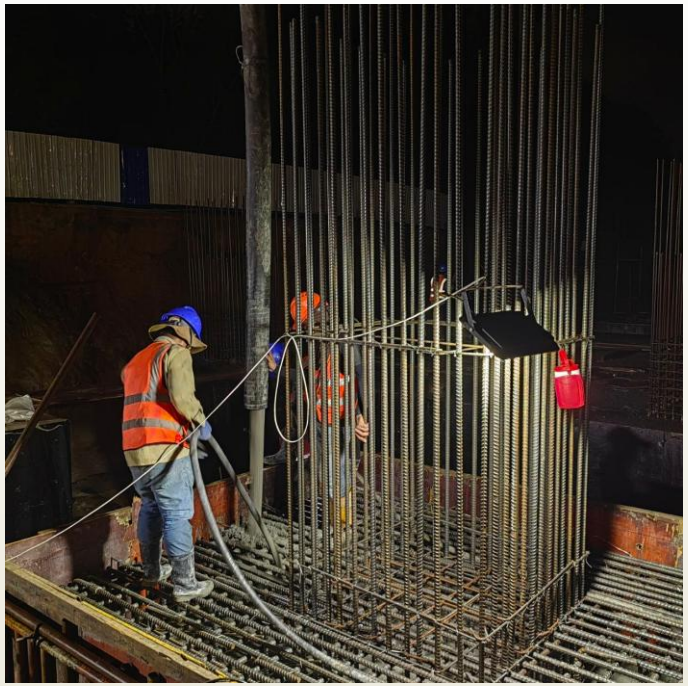

# REMOVE FORMWORK PC10 PC11 & PC12

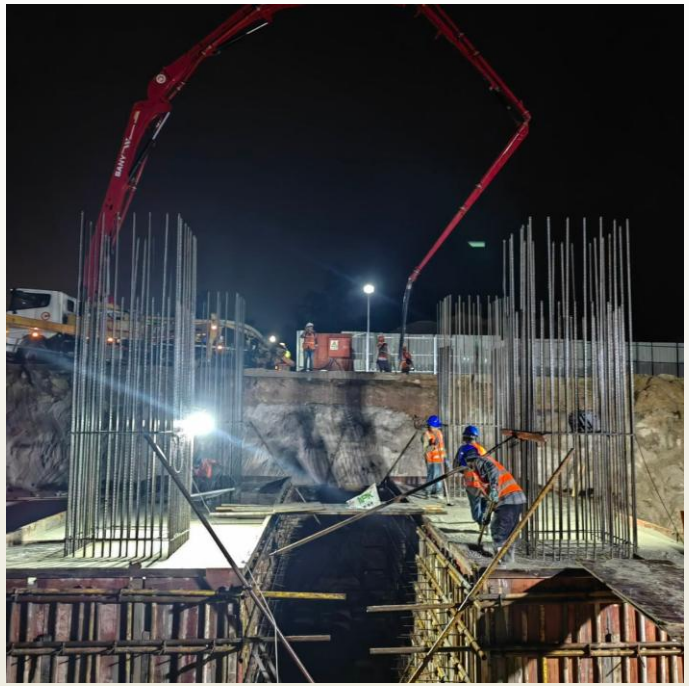





# SOIL DEPOSAL





# MATERIAL ARRIVED ON SITE









# SITE ENVIRONMENT







PASSION FOR PROGRESS!

TIME SQUARE 10

OCEAN VIEW

THE BEST DAY IN OTRES BEACH

THANK YOU!
