# Weekly Report

19. SEP. 2026

Time Square 11

# Project Location

# Time Square 11 Point Of View

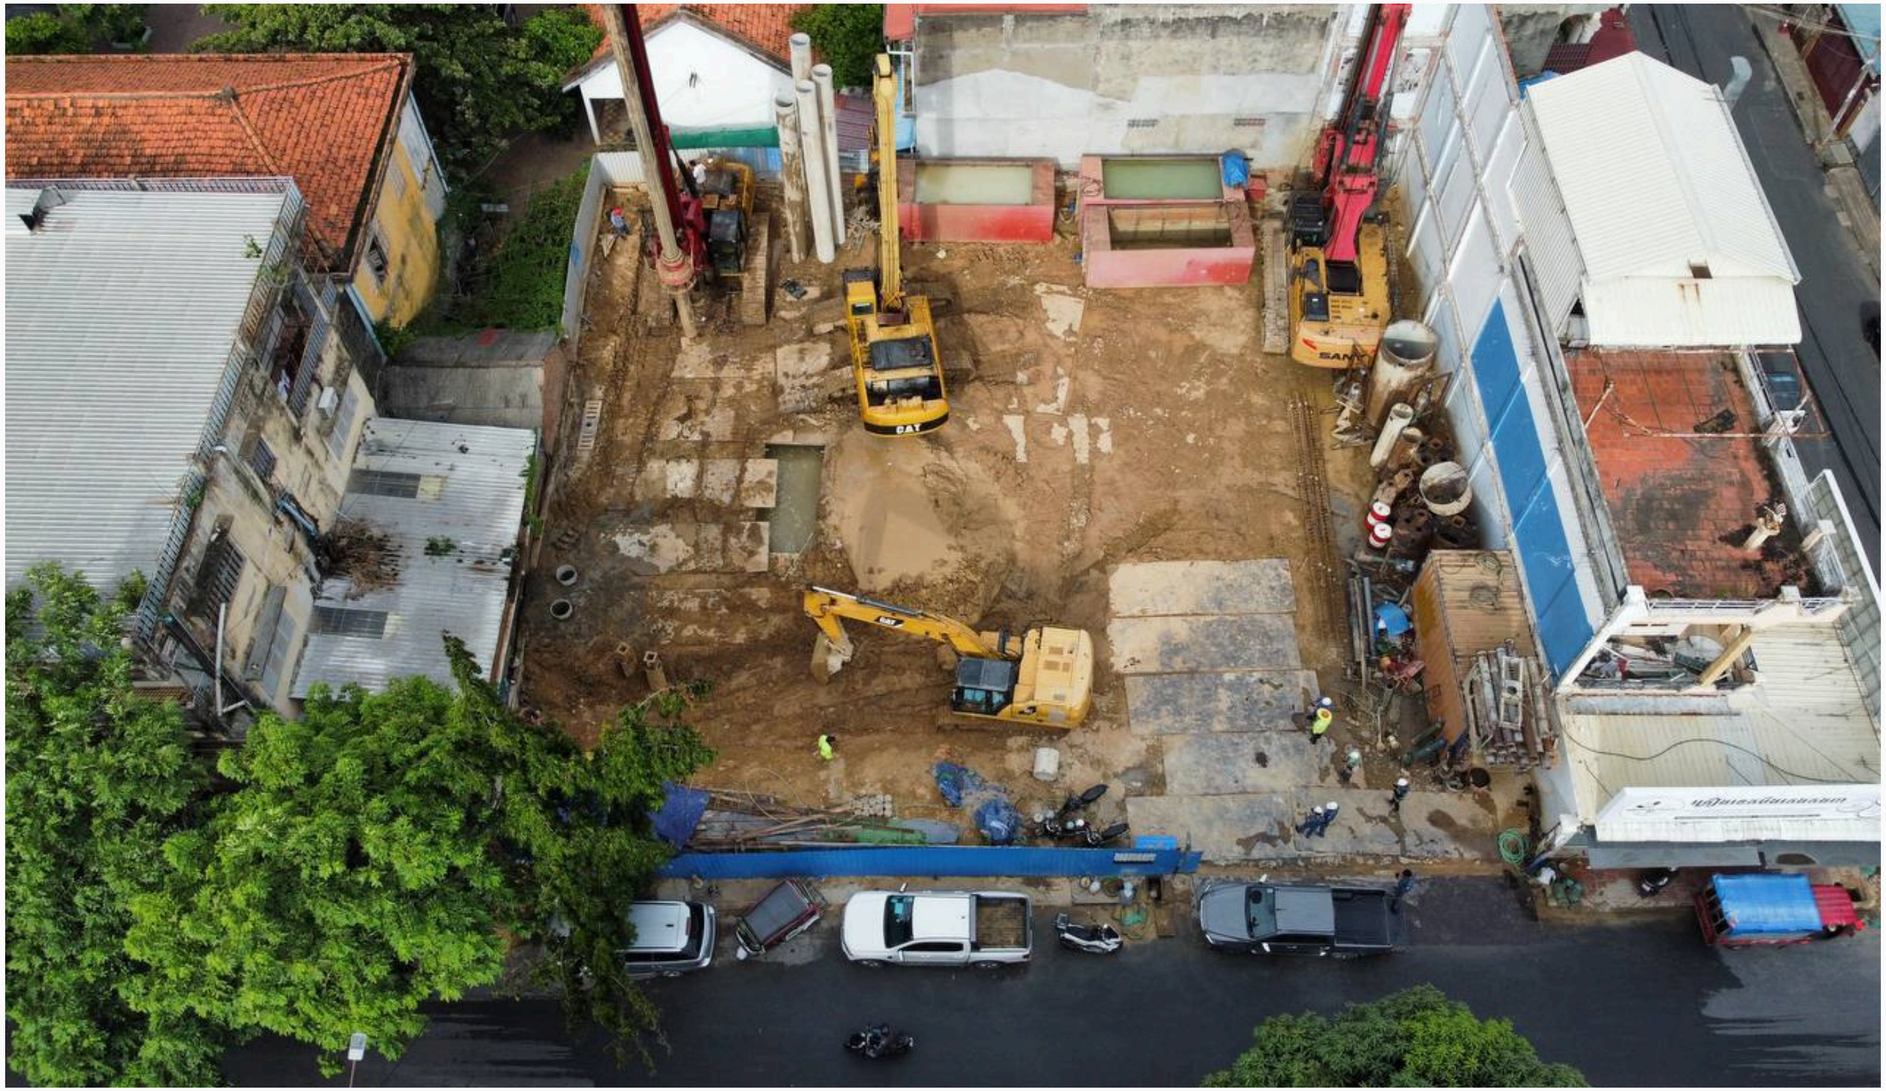

# CBP PROGRESS

## CBP PILES (168/168 PILES)

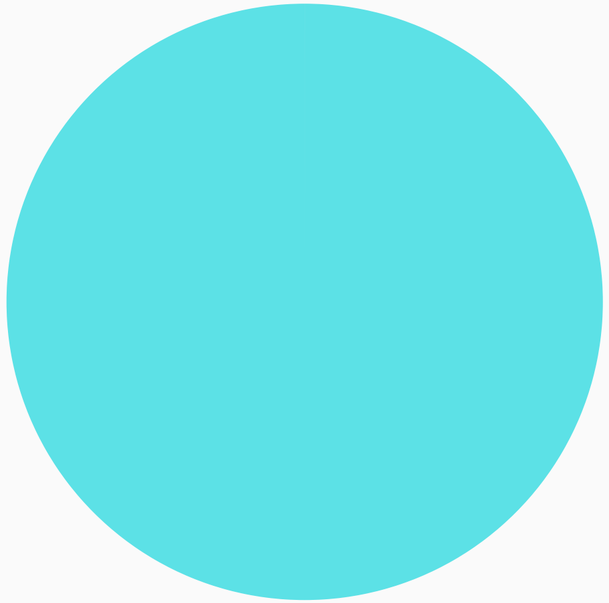

Done
100%

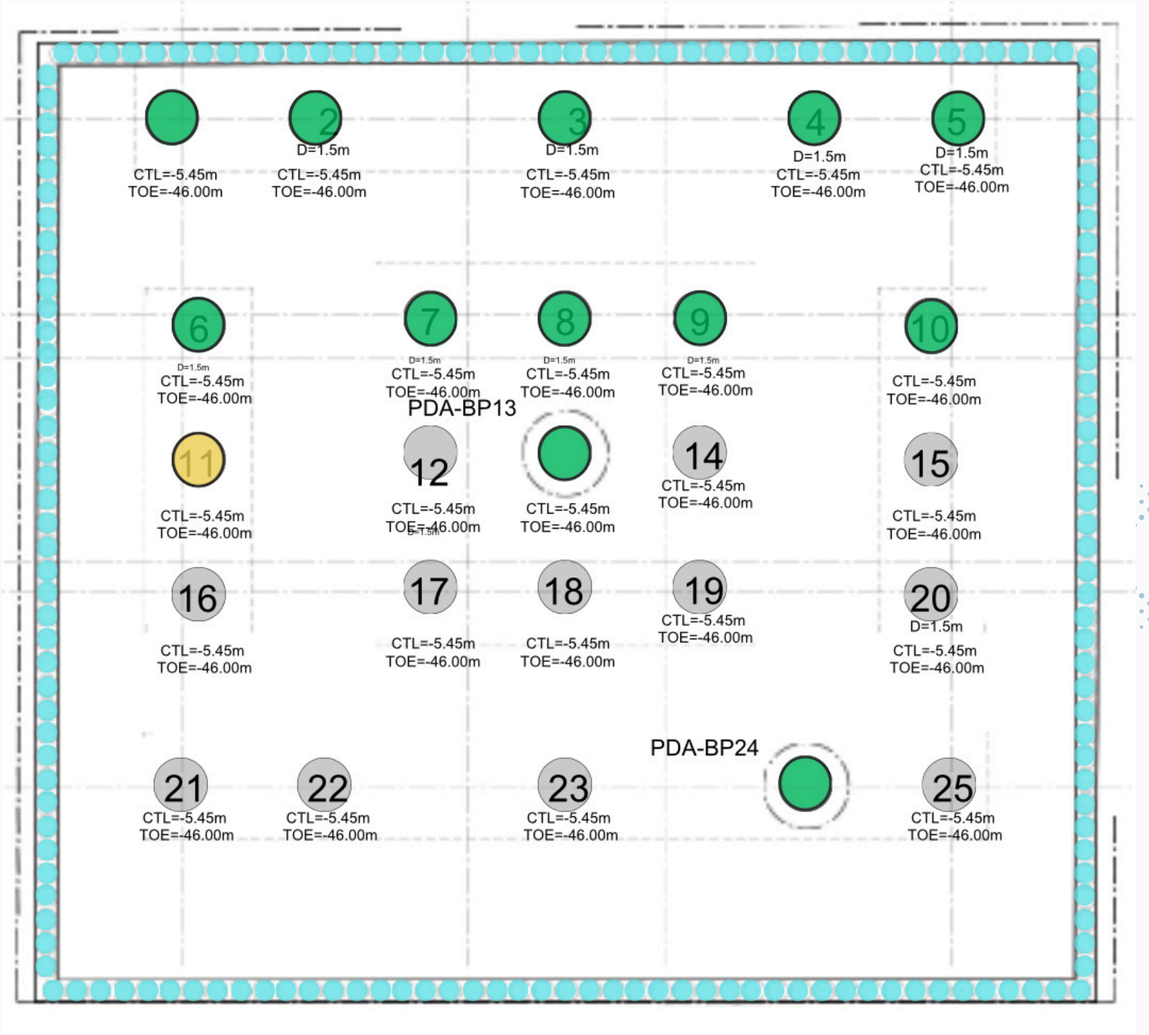

# PDA Test Progress

## PDA PROGRESS (2/2 Piles)

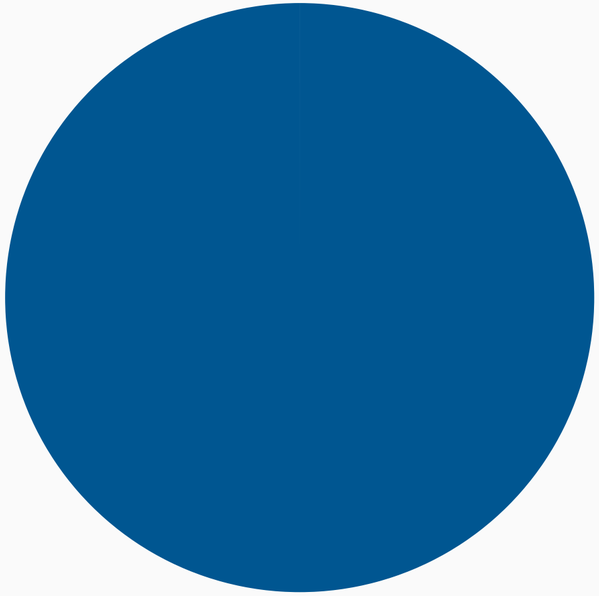

Done
100%

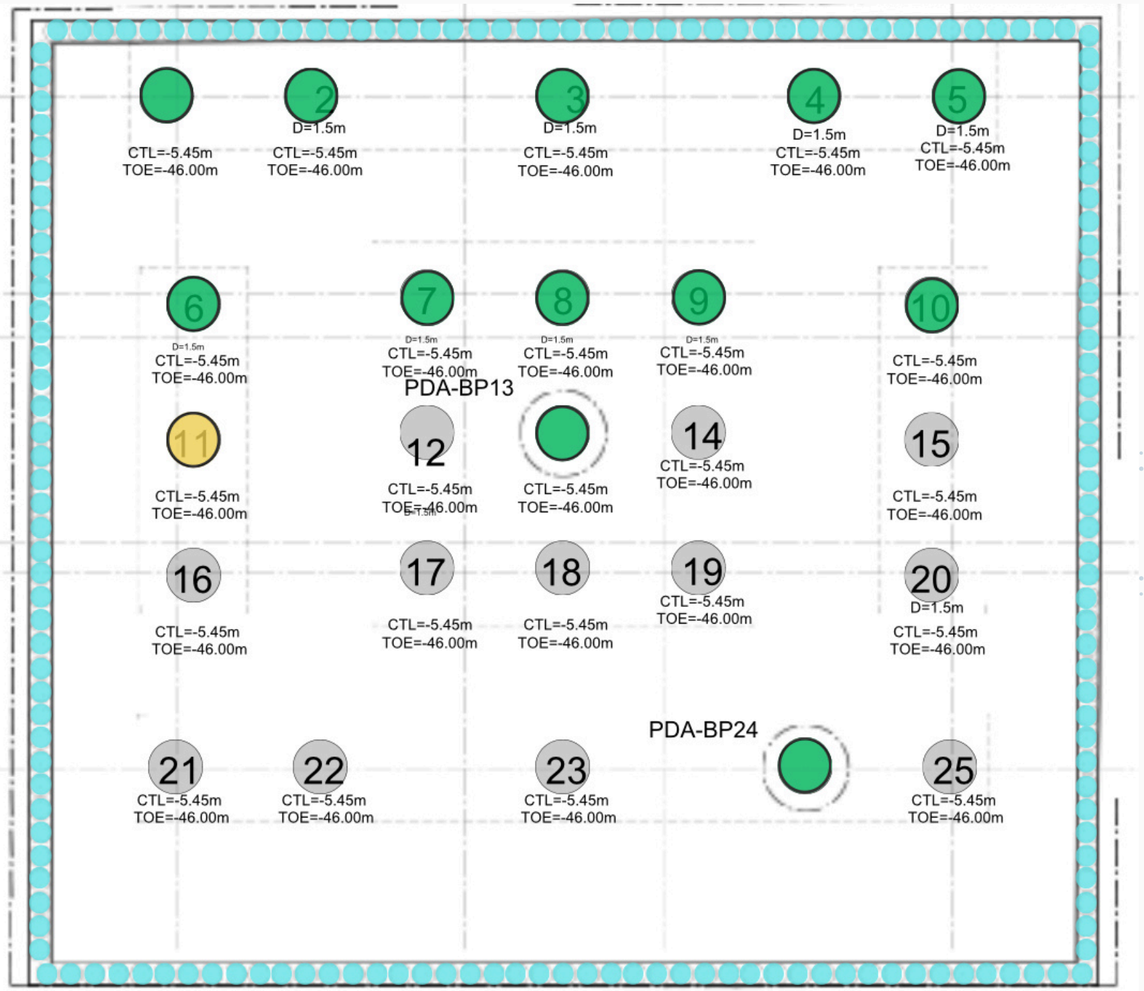

Time Square 11

# Cross-hole Sonic Progress

## Up to 19. SEP. 2026 (02/25 Piles)

### Sonic Test PROGRESS

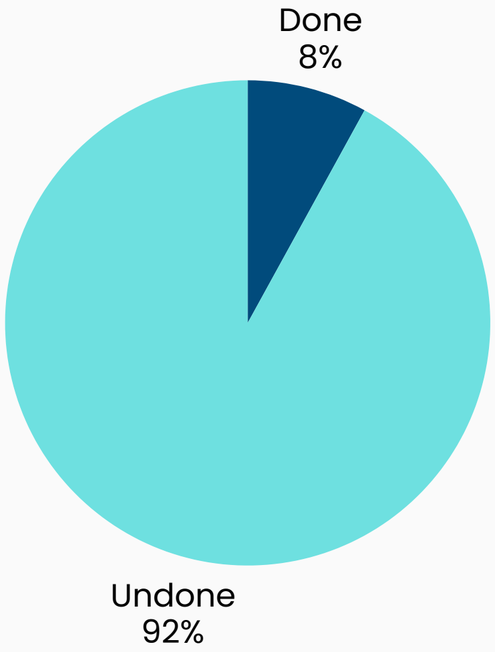


Finished Sonic testing.

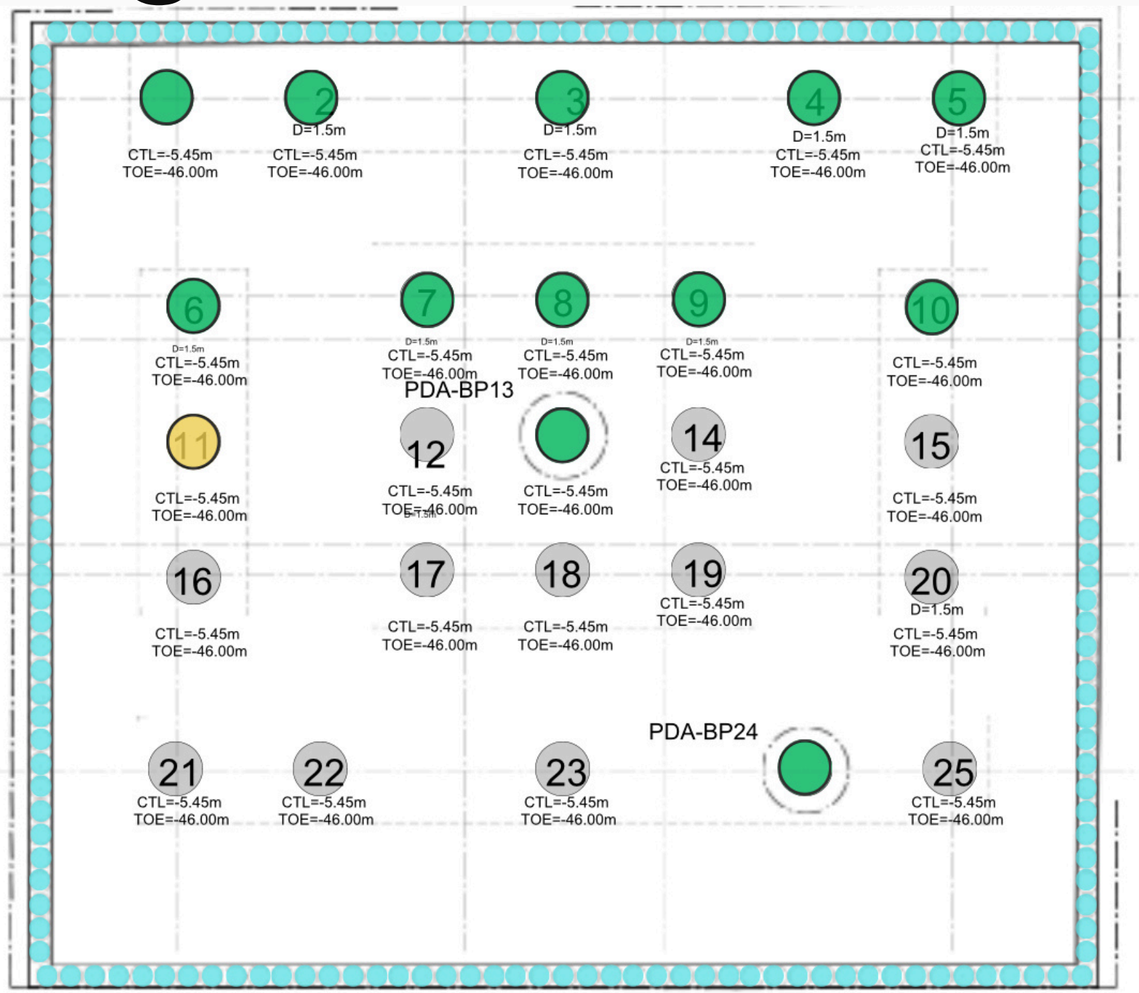

Time Square 11

# Main Pile Progress

## Up to 19. SEP. 2026 (12/25 Piles)

### Main Pile PROGRESS

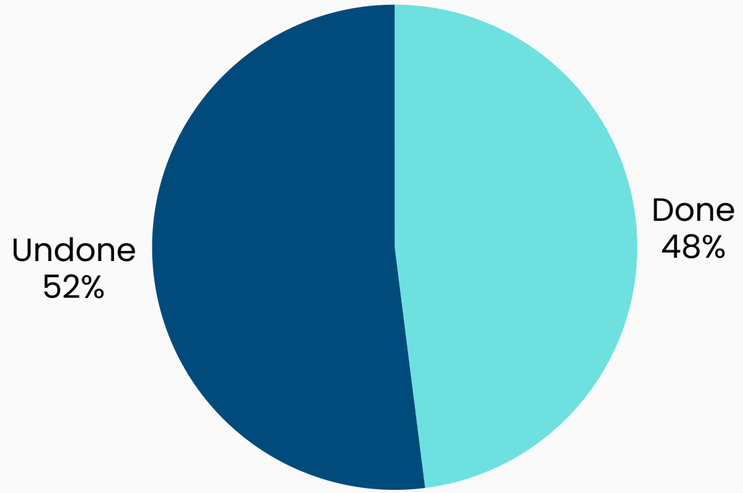


Finished Main Pile Concrete.

Unfinished Main Piles.

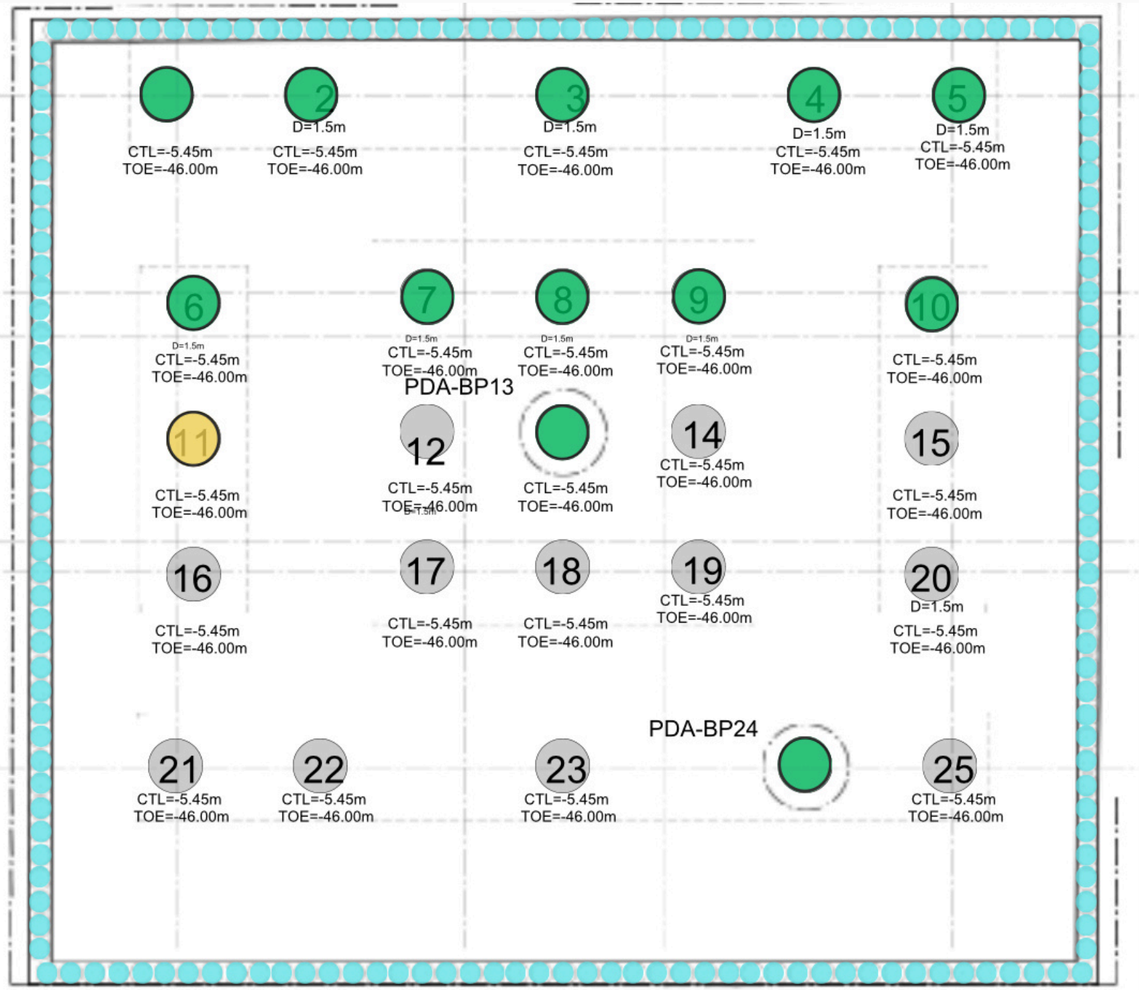

Time Square 11

# Drilling Work

# Coordinate Inspection

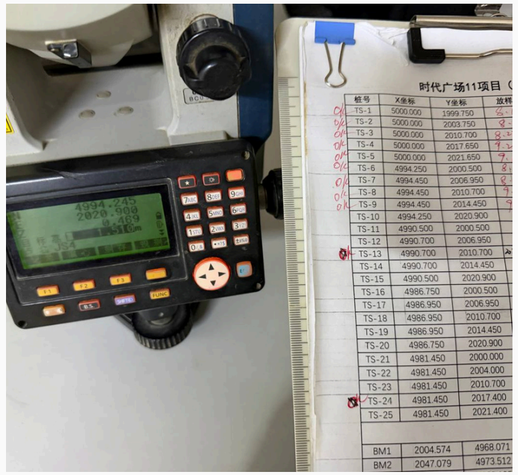


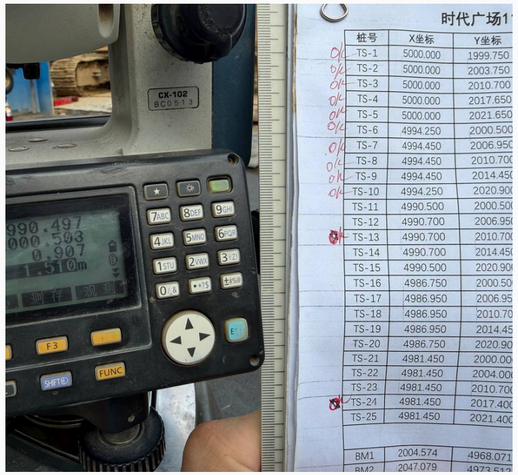


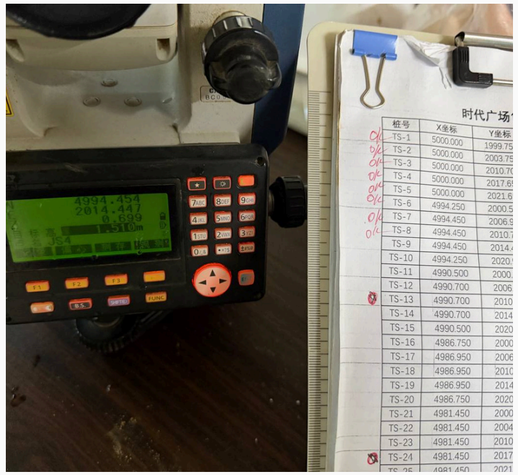

Time Square 11

# Bentonite Inspection

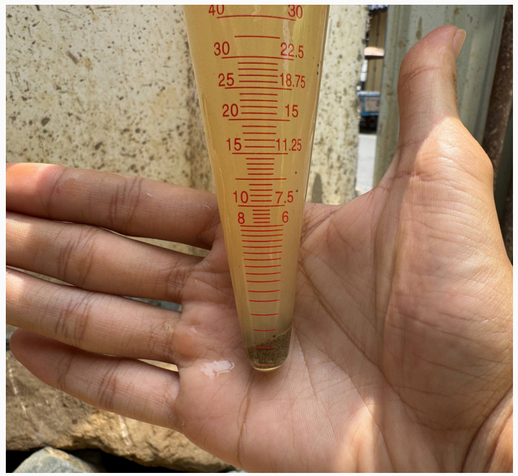

Time Square 11

# Rebar Inspection

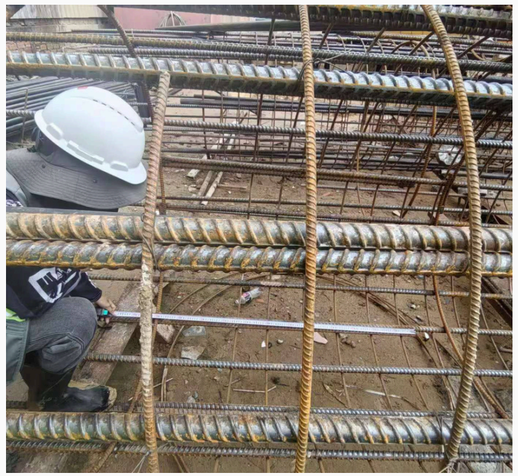

# Depth Inspection / Lowering Rebar

# Pile Cleaning

Time Square 11

# Slump Inspection

# Site Cleaning

# Soil Disposal

Time Square 11

# Passion For Progress!

**Thank You!**
