Weekly Report

19. OCT. 2026

Project Location

Time Square 11 Point Of View

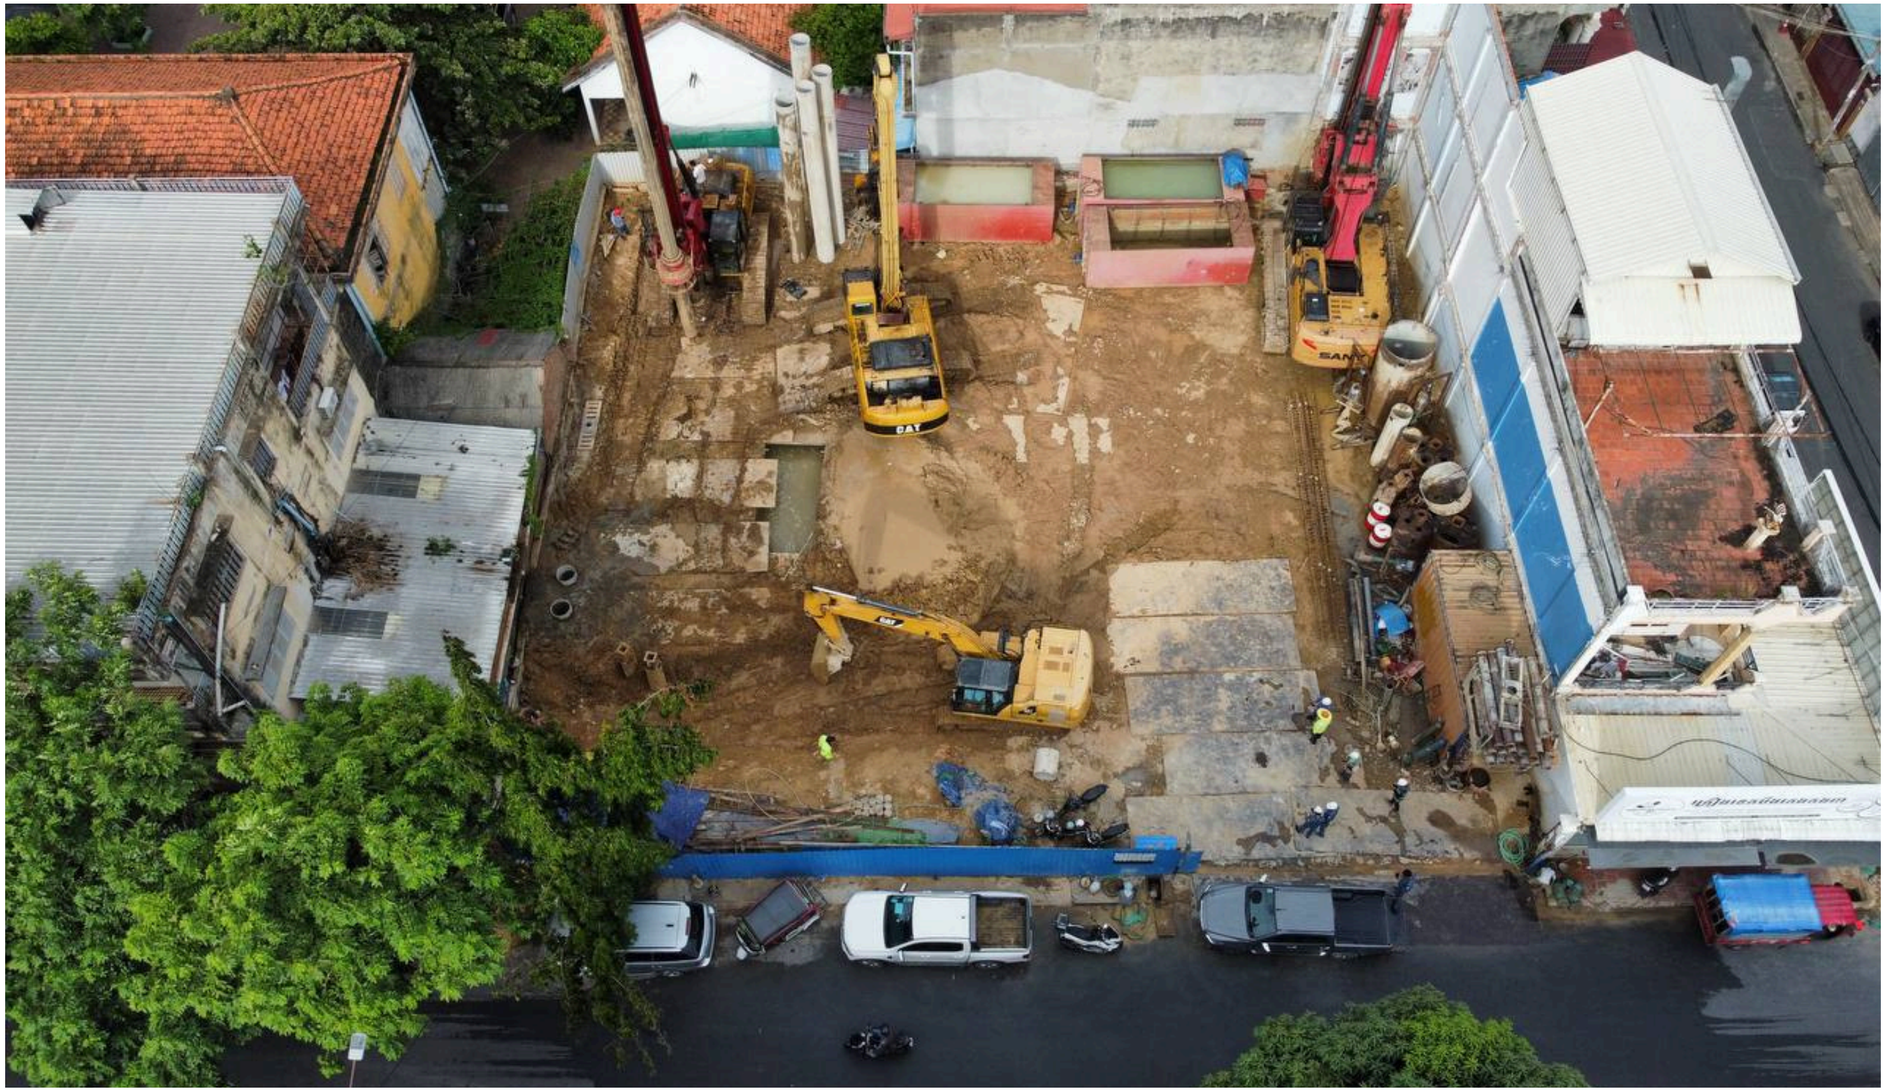

CBP PROGRESS

CBP PILES (168/168 PILES)

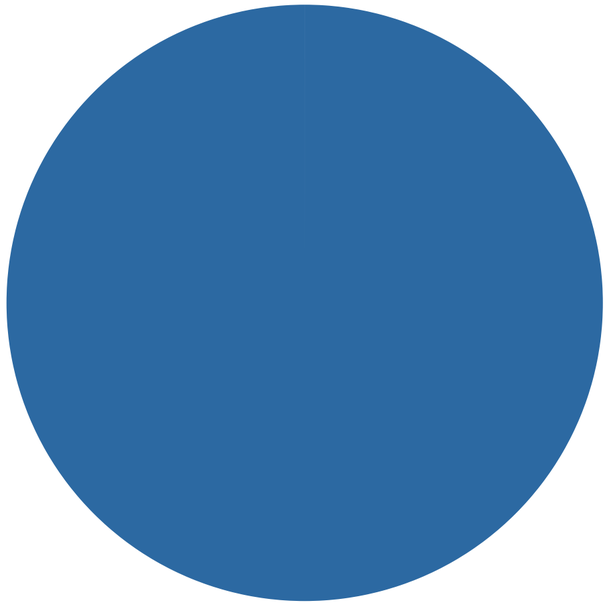

Done
100%

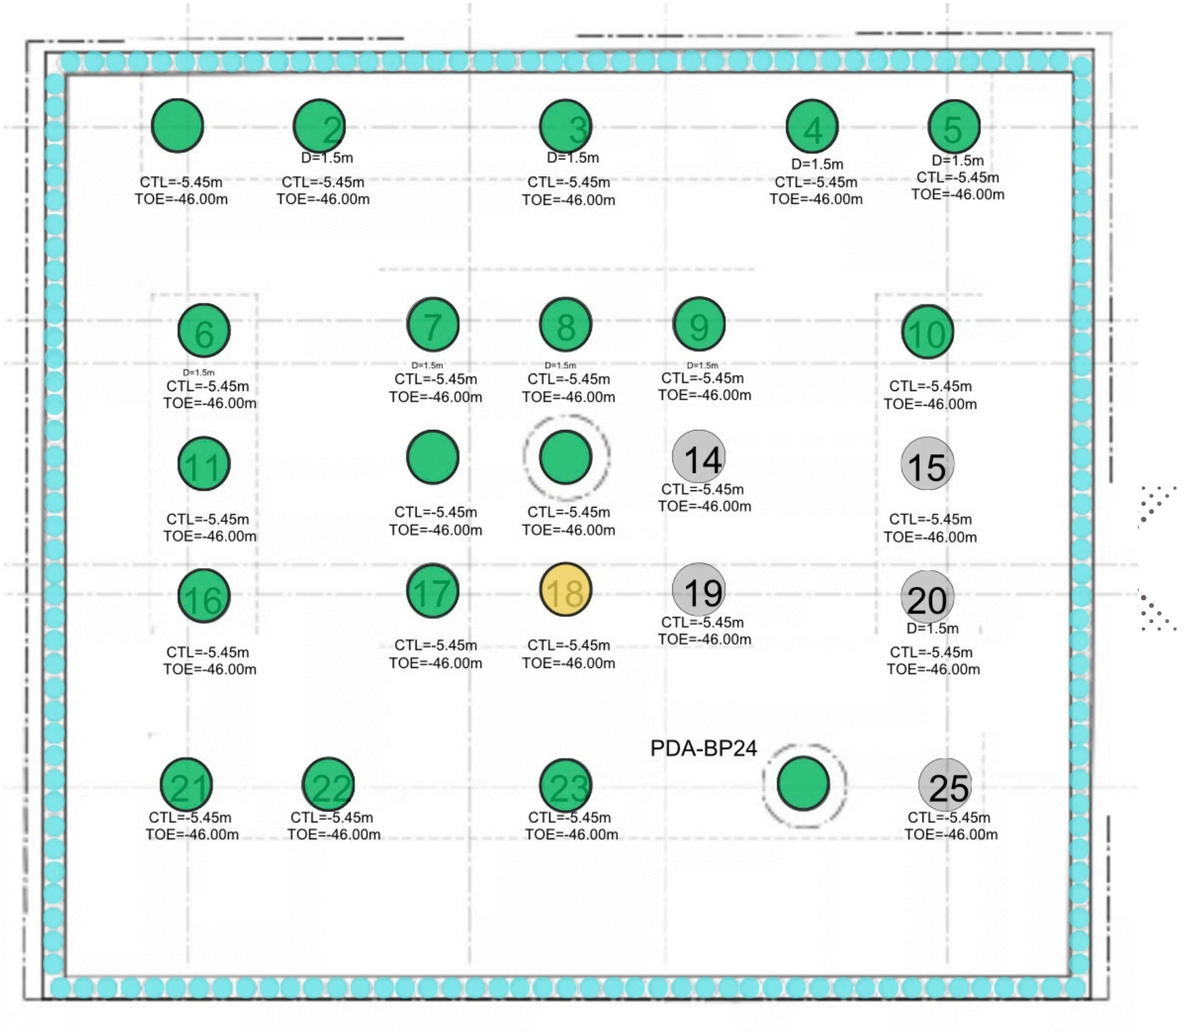

PDA Test Progress

PDA PROGRESS (2/2 Piles)

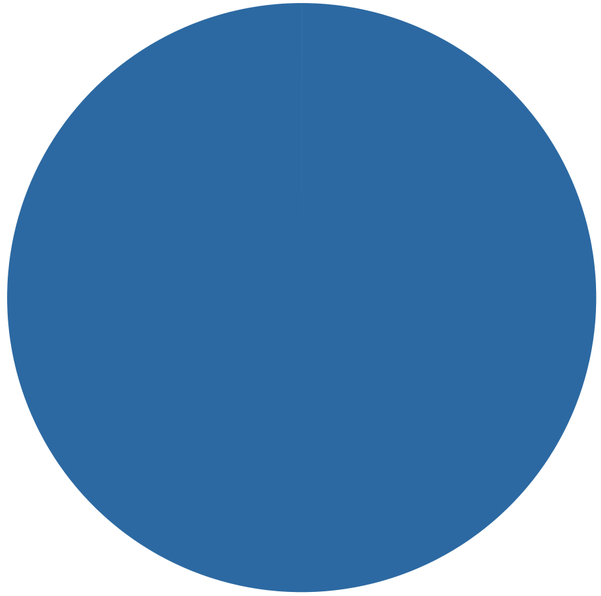

Done
100%

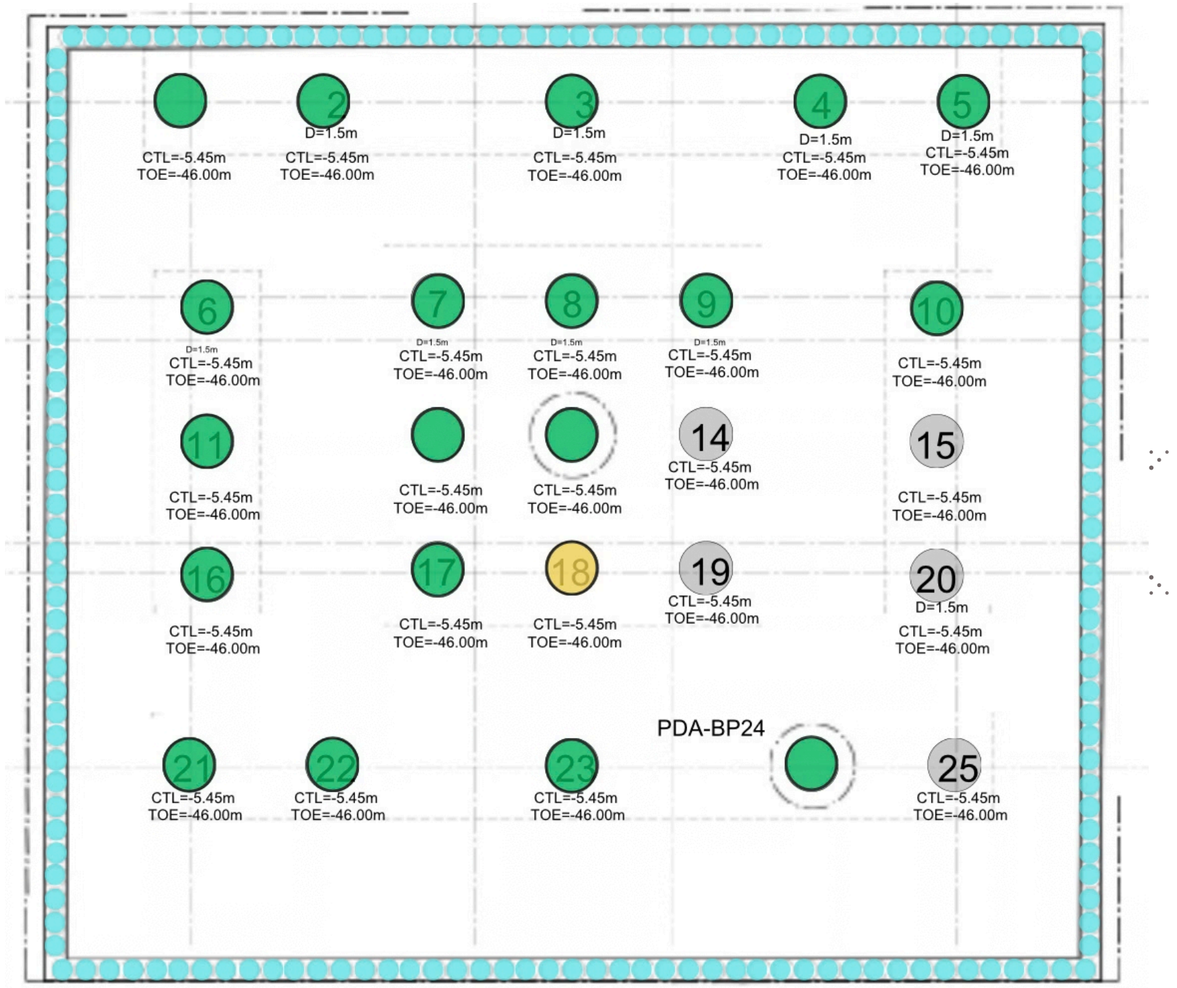

Time Square 11

Cross-hole Sonic Progress

Up to 19. Oct. 2026 (02/25 Piles)

Sonic Test PROGRESS

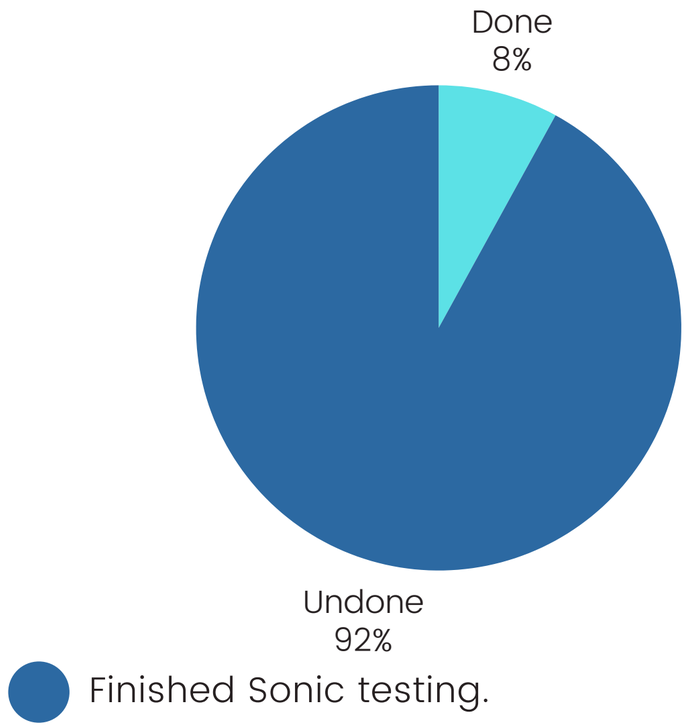

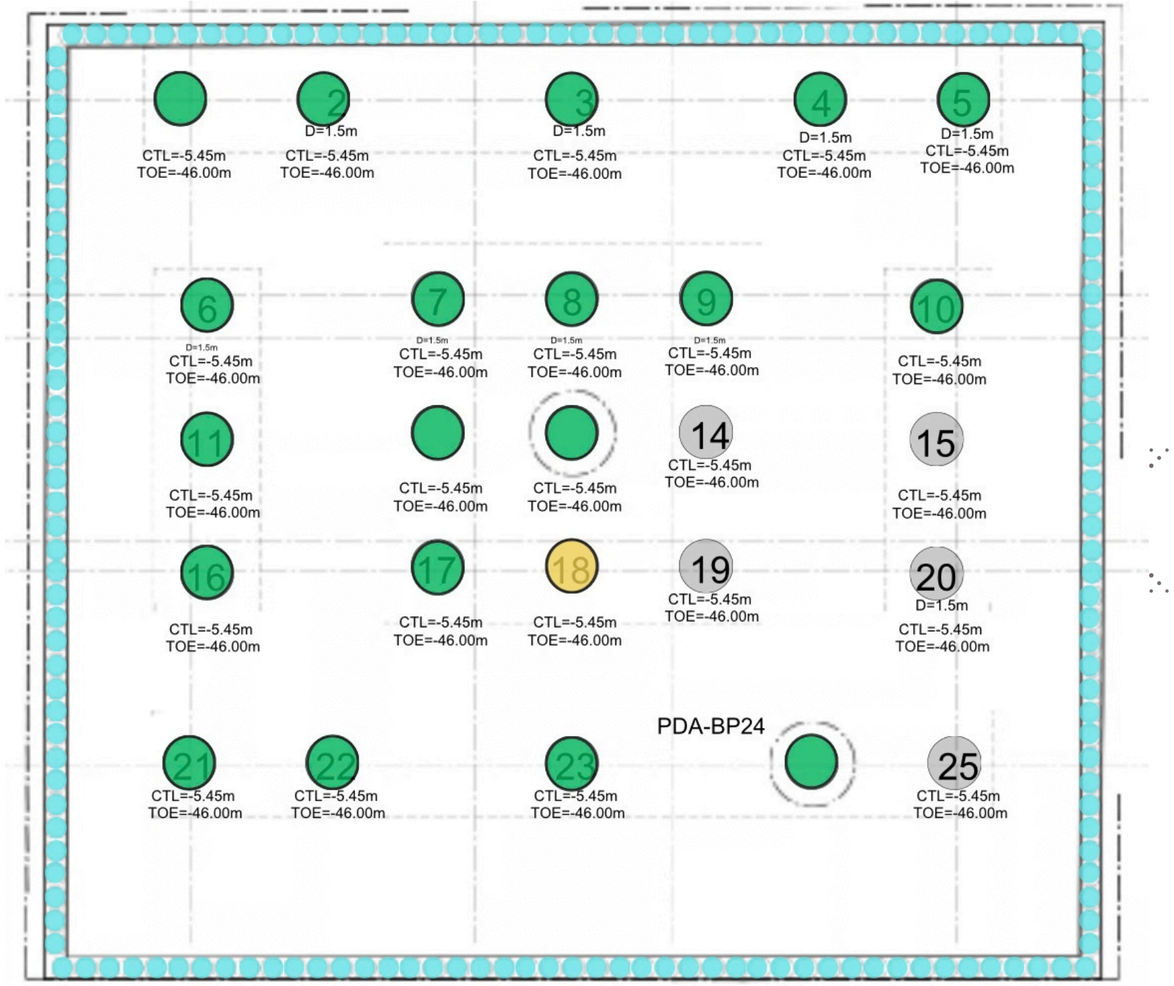

Time Square 11

Main Pile Progress

Up to 19. Oct. 2026 (20/25 Piles)

Main Pile PROGRESS

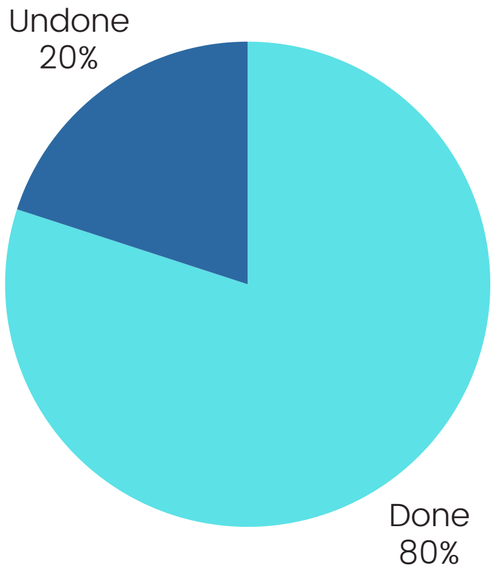

Finished Main Pile Concrete.

Unfinished Main Piles.

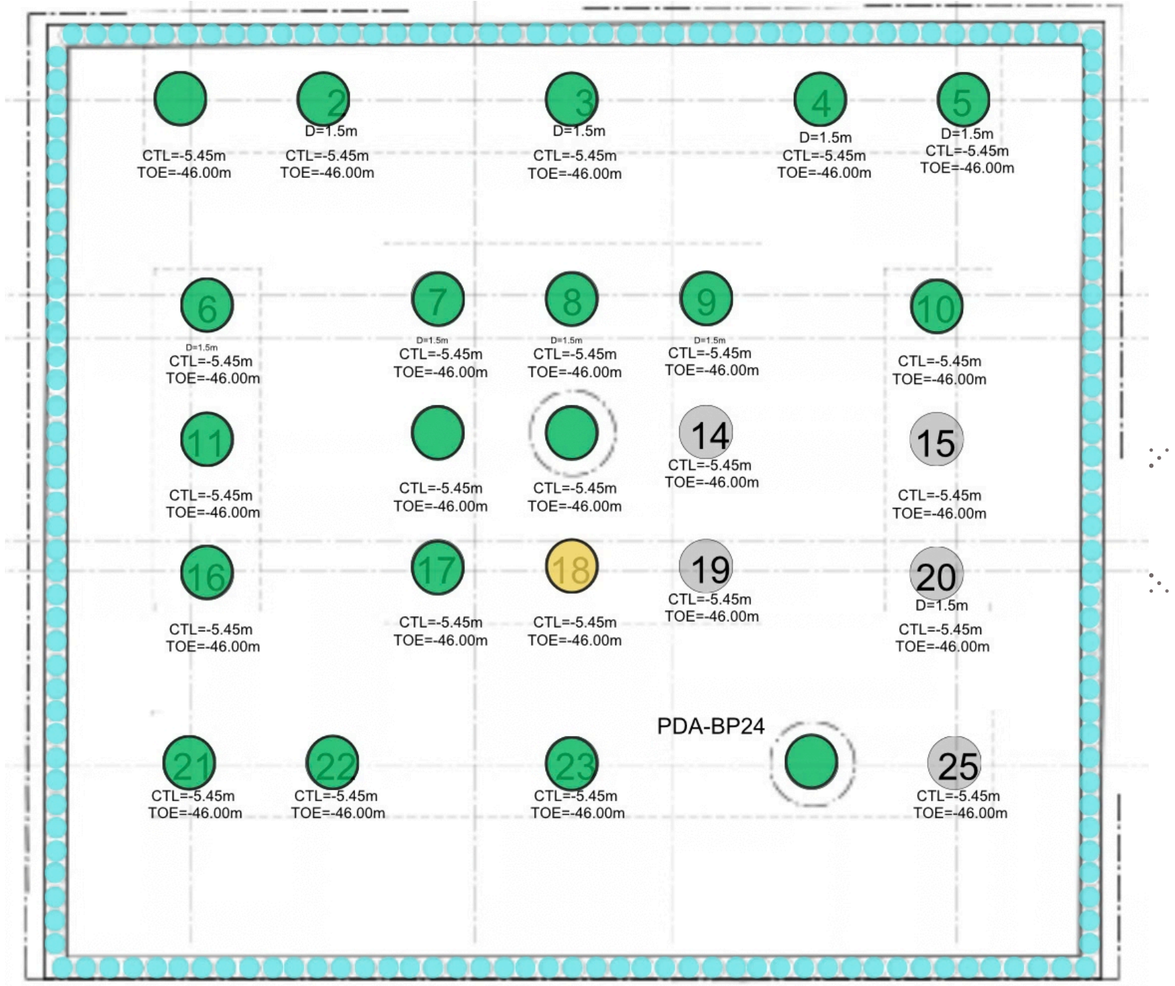

Drilling Work

Coordinate Inspection

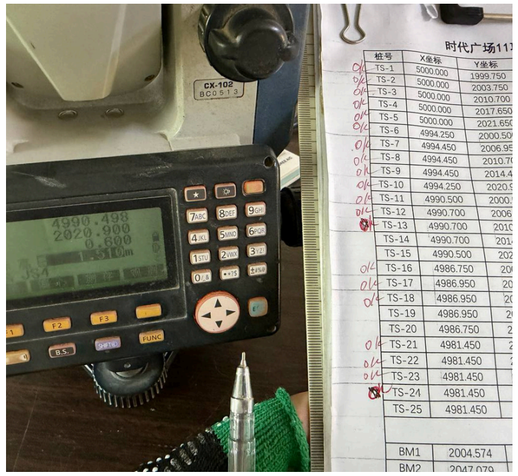

桩号	X坐标	Y坐标
TS-1	5000.000	1999.750
TS-2	5000.000	2003.750
TS-3	5000.000	2010.700
TS-4	5000.000	2017.650
TS-5	5000.000	2021.650
TS-6	4994.250	2000.500
TS-7	4994.450	2006.950
TS-8	4994.450	2010.700
TS-9	4994.450	2014.450
TS-10	4994.250	2020.900
TS-11	4990.500	2000.500
TS-12	4990.700	2006.950
TS-13	4990.700	2010.700
TS-14	4990.700	2014.450
TS-15	4990.500	2020.900
TS-16	4986.750	2000.500
TS-17	4986.950	2006.950
TS-18	4986.950	2010.700
TS-19	4986.950	2014.450
TS-20	4986.750	2020.900
TS-21	4981.450	2000.000
TS-22	4981.450	2004.000
TS-23	4981.450	2010.700
TS-24	4981.450	2017.400
TS-25	4981.450	2021.400
BM1	2004.574	4968.071
BM2	2047.079	4973.512
BM3	1962.851	4968.125
FSP1	5002.661	2023.653
FSP2	4966.380	1995.702
FSP3	5002.859	2015.825

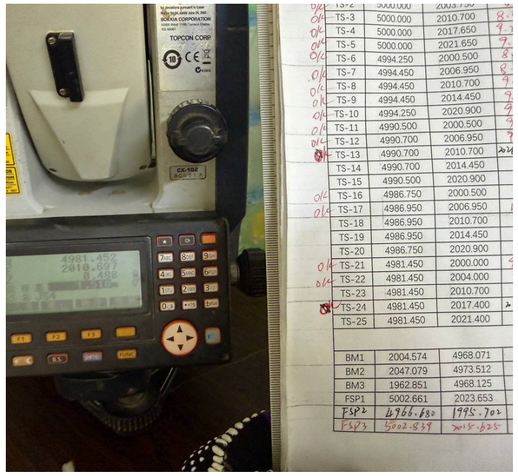

Bentonite Inspection

Rebar Inspection

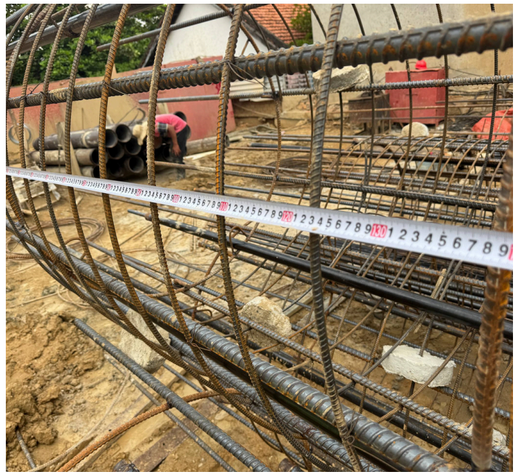

Depth Inspection / Lowering Rebar

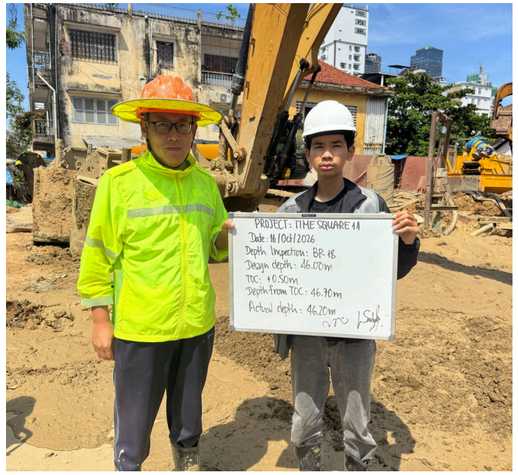

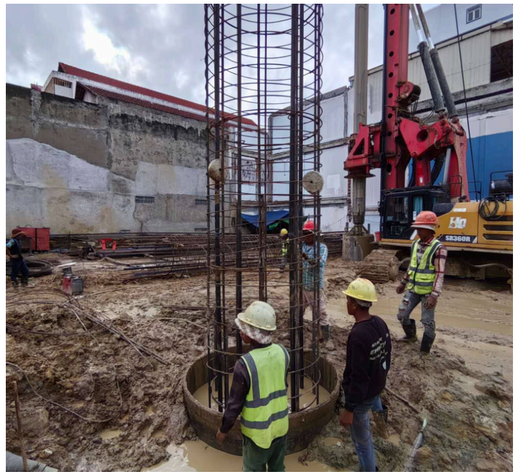

Pile Cleaning

Slump Inspection

Casting Concrete

Site Cleaning

Soil Disposal

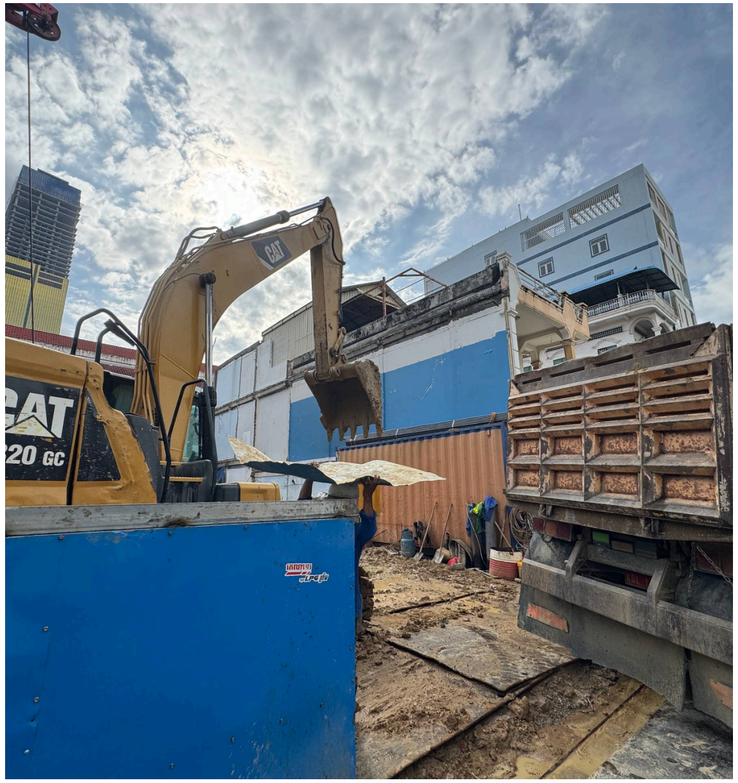

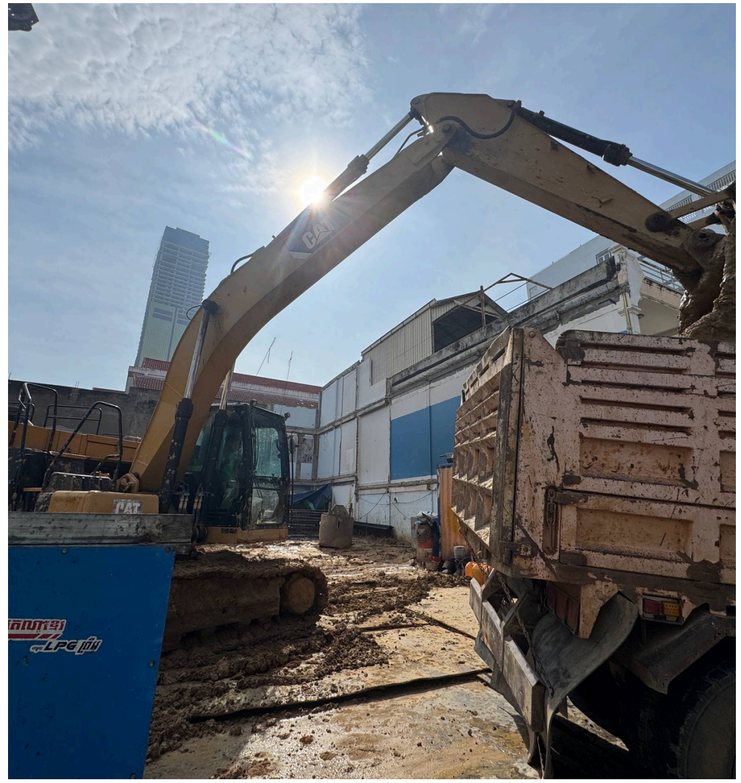

Passion For Progress!

Thank You!
